

# BRENTWOOD BOROUGH SCHOOL DISTRICT

## NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE




**HHSDR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC

# Foundation, Masonry, & Steel Progress

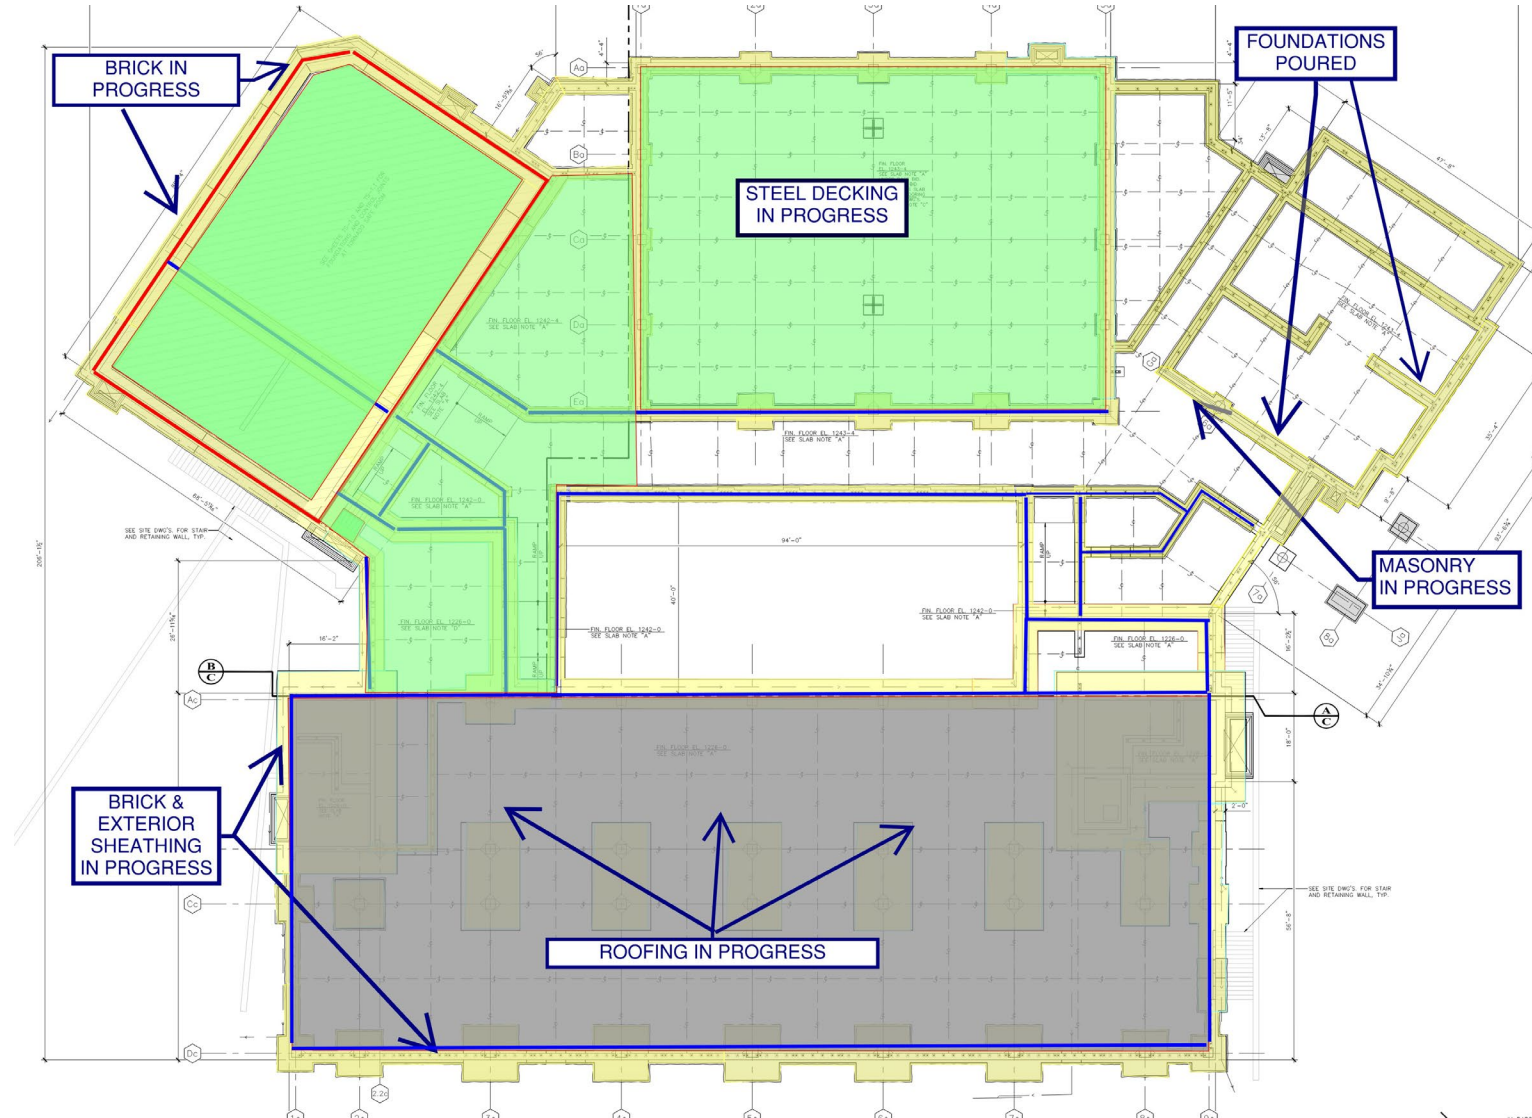



# Foundations in Areas A



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Brick Progress – Tenting for Work with Cold Temps



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Steel Progress



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Metal Framing in Storm Shelter / Cafeteria



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC




# Area C – Ground Floor – Overall Progress



Rough In Progress:

- Plumbing - 85%
- Fire Protection – 15%
- Mechanical – 95%
- Electrical – 90%

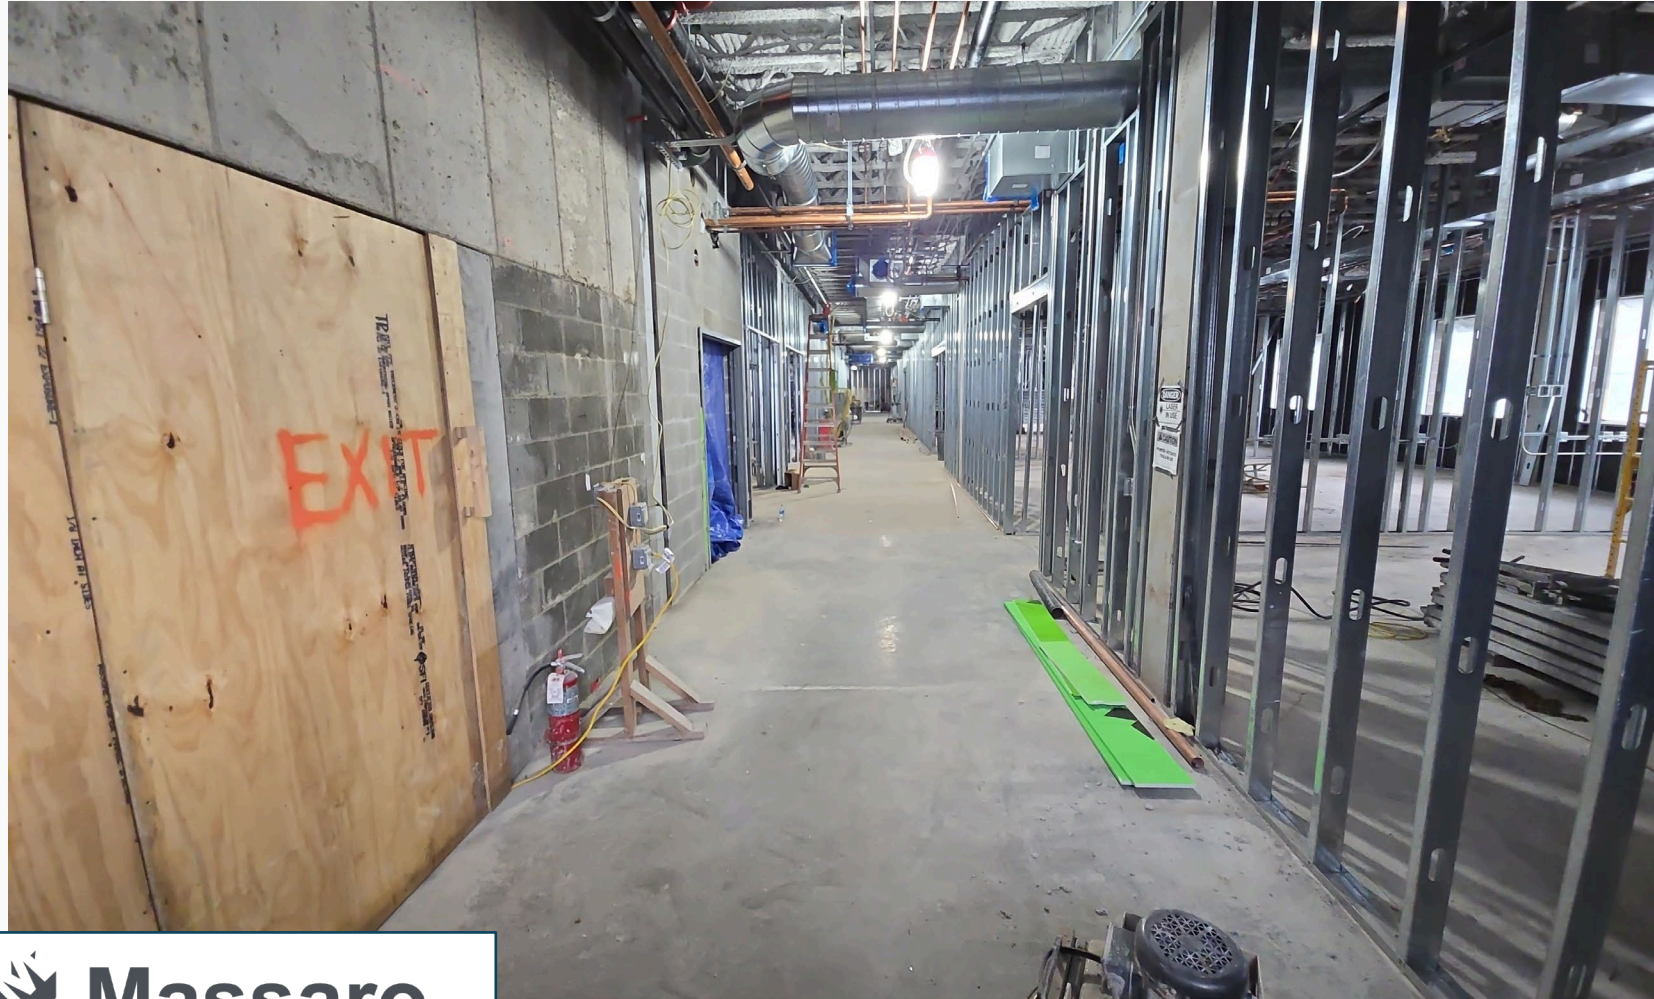

**HHSDR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Area C – 1<sup>st</sup> Floor – Overall Progress



Rough In Progress:

- Plumbing - 60%
- Mechanical – 95%
- Electrical – 60%



**HHSDR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Area C – 2<sup>nd</sup> Floor – Overall Progress



Rough In Progress:

- Plumbing - 30%
- Mechanical – 95%
- Electrical – 40%



**HHSDR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Area C – 3<sup>rd</sup> Floor – Overall Progress



Rough In Progress:

- Plumbing - 20%
- Mechanical – 60%
- Electrical – 20%



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Area C – Roofing



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Area C – Exterior Sheathing



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Middle School Career Day



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# Additional Project Information – Safety Items



## OSHA Visit

- On Tuesday, November 18, 2025, an OSHA inspector made a random visit to our project site.
- The inspector returned for a follow up visit on November 25, 2025.
- Although he completed an extremely thorough inspection and there were a number of items to correct, he was very satisfied with the efforts made by all the contractors.

## Stop Work

- On Friday, 12/5/2025, MCMS had to stop work in the building due to a safety concern associated to the masons scaffolding and its proximity to the Duquesne Light service.
- Duquesne made the necessary changes to the service to make the site safe and an all clear was given within the same day.



**HHS DR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



# OVERALL PROGRESS



## Upcoming Work:

- Complete steel decking at gym
- Continue Mechanical, Electrical, and Plumbing Rough In at Area C
- Complete exterior sheathing at Area C
- Complete roofing at Area C
- Continue Area B framing
- Area B rough ins
- Continue block and brick installation

## Project Schedule

- We have not received the schedule update from Mucci to date. There are some concerns regarding the schedule related to getting the building enclosed and heated.



## Project Stats:

- Project is at 14 day with no recordable injury



**HHSDR**  
ARCHITECTS  
ENGINEERS



**Massaro**  
CM SERVICES, LLC



**HAVE A WONDERFUL  
HOLIDAY!**

QUESTIONS?

