

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE



HHSDR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Mock Up



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

6/9/25 11:15:13 AM EDT

Continue Concrete Foundations



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Installation – Stair 2



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Installation – Stair 1 & Elevator



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Mechanical Room – Floor and Equip. Pads Poured



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

5/27/25 2:43:29 PM EDT


Masonry Installation – Exterior Wall along Willock Road



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

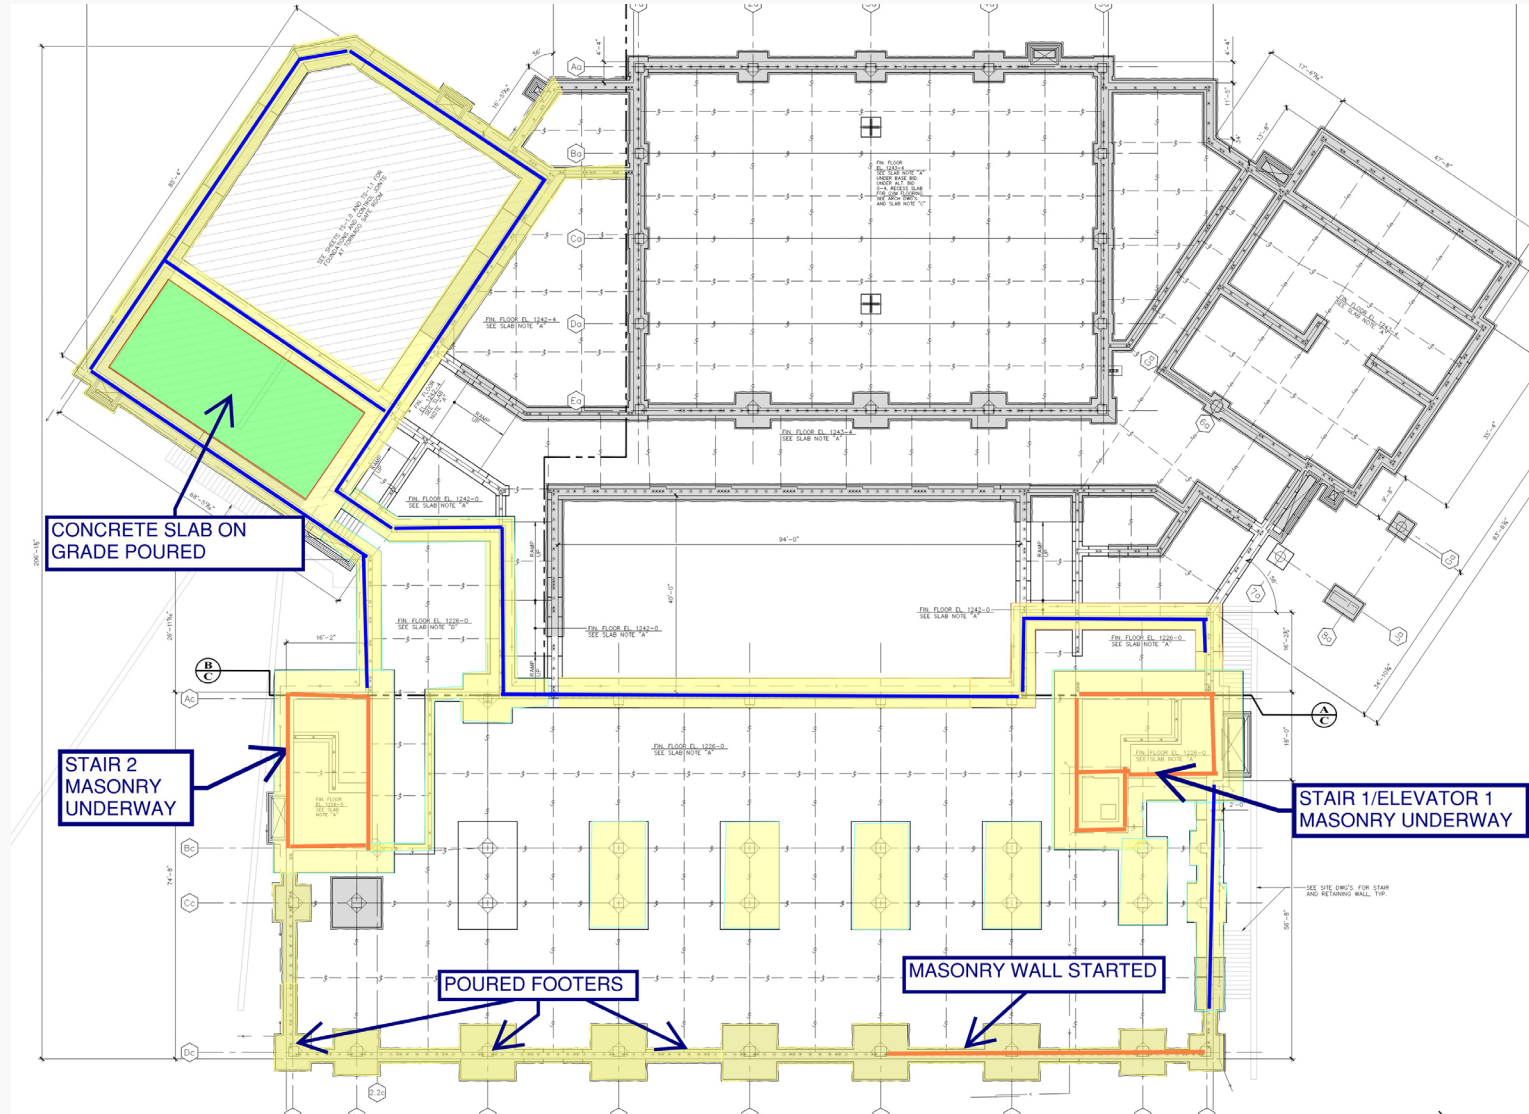

Stairs to mechanical room from basement level formed



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Water Proofing and Backfilling Foundation Walls



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Transformer Precast Pad Set



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

6/5/25 2:00:12 PM EDT

OVERALL PROGRESS



Upcoming Work:

- Start foundations in Area A
- Finish MEP Coordination
- Complete masonry installation at Stairs 1 & 2.
- UG Plumbing & Electric in Area C
- Storm line installation
- Continue Backfill Foundation Walls
- Steel Erection to start in June

Project Schedule

- Mucci will complete a project schedule update for June 13, 2025. The project remains on schedule for substantial completion on August 14, 2026



Project Stats:

- Project is at 16 days with no recordable injury



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU

QUESTIONS?

