

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Admin Area Roof Complete



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Admin Waiting Area



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Principal's Offices



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Admin Conference Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Health Suite



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Gym



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – IDF, Storage & Restrooms



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A



- CMU - 90%
- Brick - 65%
- Structural Steel - 95%
- Admin Roofing - 100%
- Concrete Slab on Grade pours are ongoing
- Roof Drains - 80%
- Framing - 50%
- MEP Rough Ins - 40%



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Main Corridor




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area B – Storm Shelter / Cafeteria

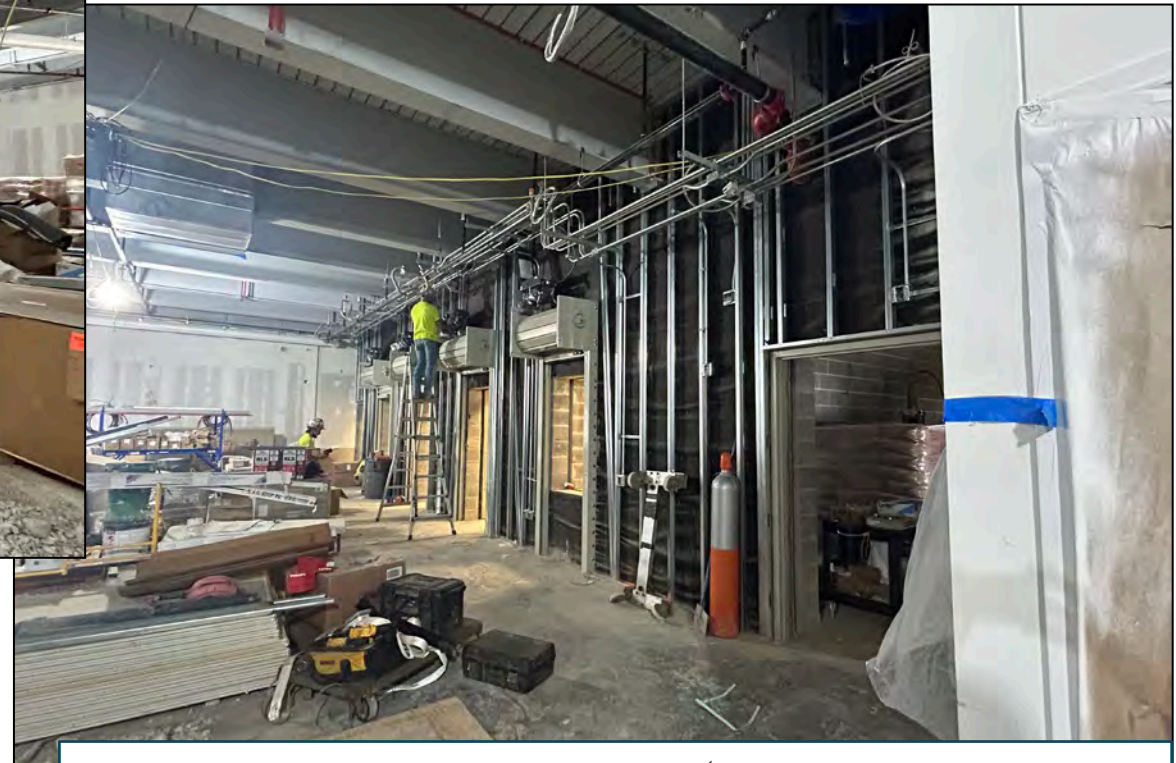

- Drywall – 85%
- Rolling Doors – 75%
- MEP Rough ins – 95%
- Painting – 20%
- Windows – 50%



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area B – Kitchen



- Ceramic Tile – 95%
- Kitchen Hood Installed
- Ceiling Grid – 80%
- MEP Trim – 50%



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Typical Classroom




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Art Classroom

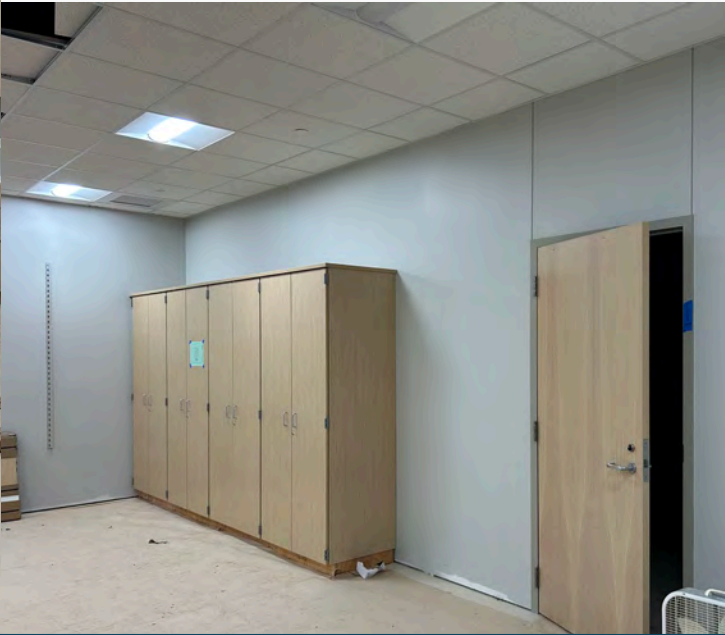

Area C Ground Floor – Kiln & Storage Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Music Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Music Storage Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Restrooms




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Restrooms

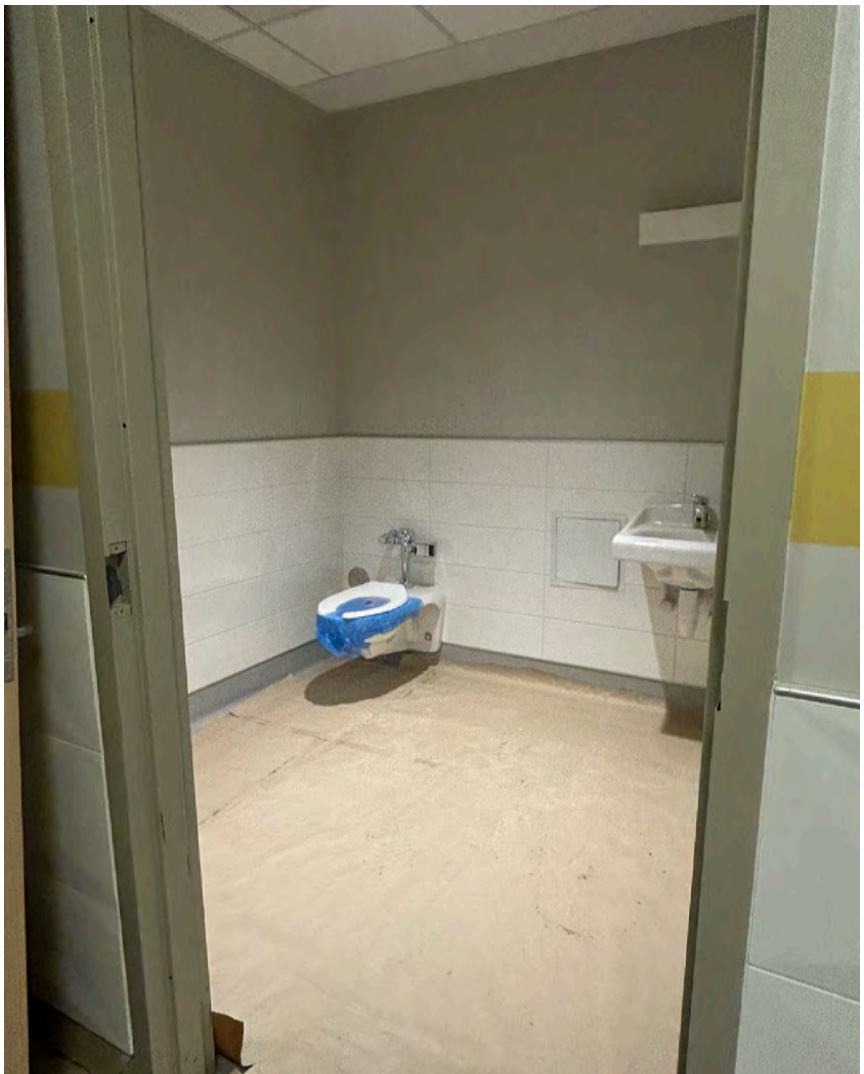

HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC



Area C Ground Floor – MDF



Jun 15, 2026 at 10:40 AM EDT



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Ground Floor – Overall Progress



Ceilings – 90%

Flooring – 60%

Casework – 75%



	HHSDR ARCHITECTS ENGINEERS		Massaro CM SERVICES, LLC
---	---	---	------------------------------------

Area C 1st Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Title 1



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Life Skills



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Restrooms



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Media Center



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Media Center from Corridor



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Corner Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Learning Support



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 1st Floor – Overall Progress



Painting & Ceramic Tile – 95%

Ceilings – 95%

Light Fixtures - 99%

Flooring – 50%

Casework – 25%



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Corner Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Counseling




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Restrooms

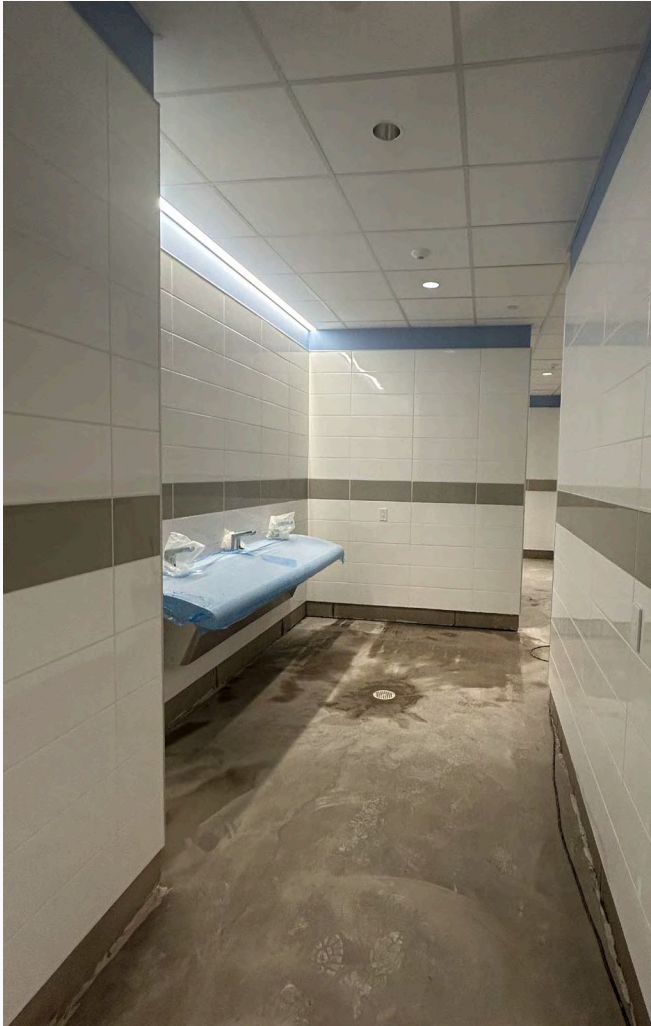

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 2nd Floor – Overall Progress



Painting & Ceramic Tile – 95%

Ceilings – 95%

Lighting – 95%

Flooring – 10%



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 3rd Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 3rd Floor – Corner Classroom




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 3rd Floor – Restrooms

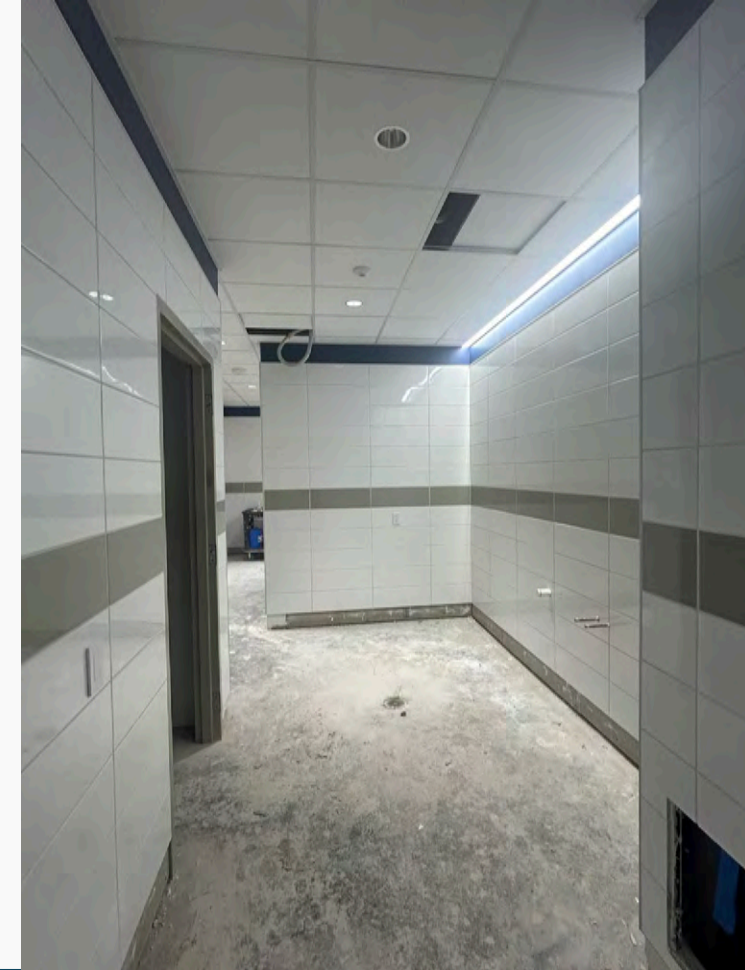

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 3rd Floor – Overall Progress



Painting & Ceramic Tile – 95%

Windows – 85%

Ceilings – 90%

Lighting – 90%



HHS DR
ARCHITECTS
ENGINEERS




Massaro
CM SERVICES, LLC

Area C – Roof



Playground surfacing materials delivered today

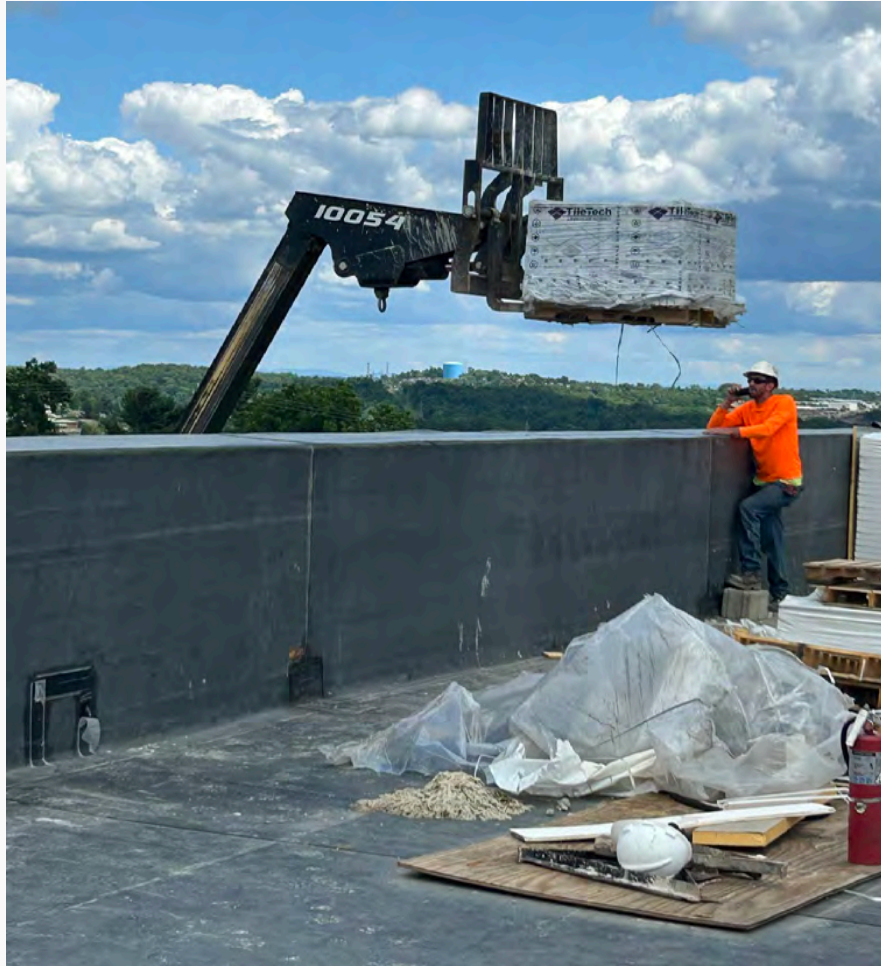

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Roof – Restroom & Storage



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Stairwell 1



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Brick Progress – Gym



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC



Area B – Brick Progress - Admin



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Storm Work – Foundation for Site Wall



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

OVERALL PROGRESS



Upcoming Work:

- Finish Drywall in Area B
- Complete Painting in Area B
- Start Kitchen Equipment
- Area A – Gym & Main Corridor Roofing
- Area A – Corridor Fireproofing
- Continue Mechanical, Electrical and Plumbing Rough In at Area A
- Continue Flooring in Area C
- Finish Plumbing Fixtures in Area C
- Complete Window installation at Area C
- Window installation in Areas A & B
- Complete block and brick installation
- Concrete Slab on Grade in Corridor & Gym
- Complete Grading in Courtyard
- Complete Site Wall
- Playground Surfacing

Project Schedule

- Mucci's schedule update dated 6/5/2026 was reviewed with the Board last week. No new update has been received.



Project Stats:

- Project is at 166 day with no recordable injury



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU!

QUESTIONS?

