

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Mock Up



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

5/19/25 9:42:26 AM EDT

Continue Concrete Foundations



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Continue Concrete Foundations



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Installation – Stair 1 & Elevator



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Installation – Stair 2




HHSR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Foundation & Masonry Progress

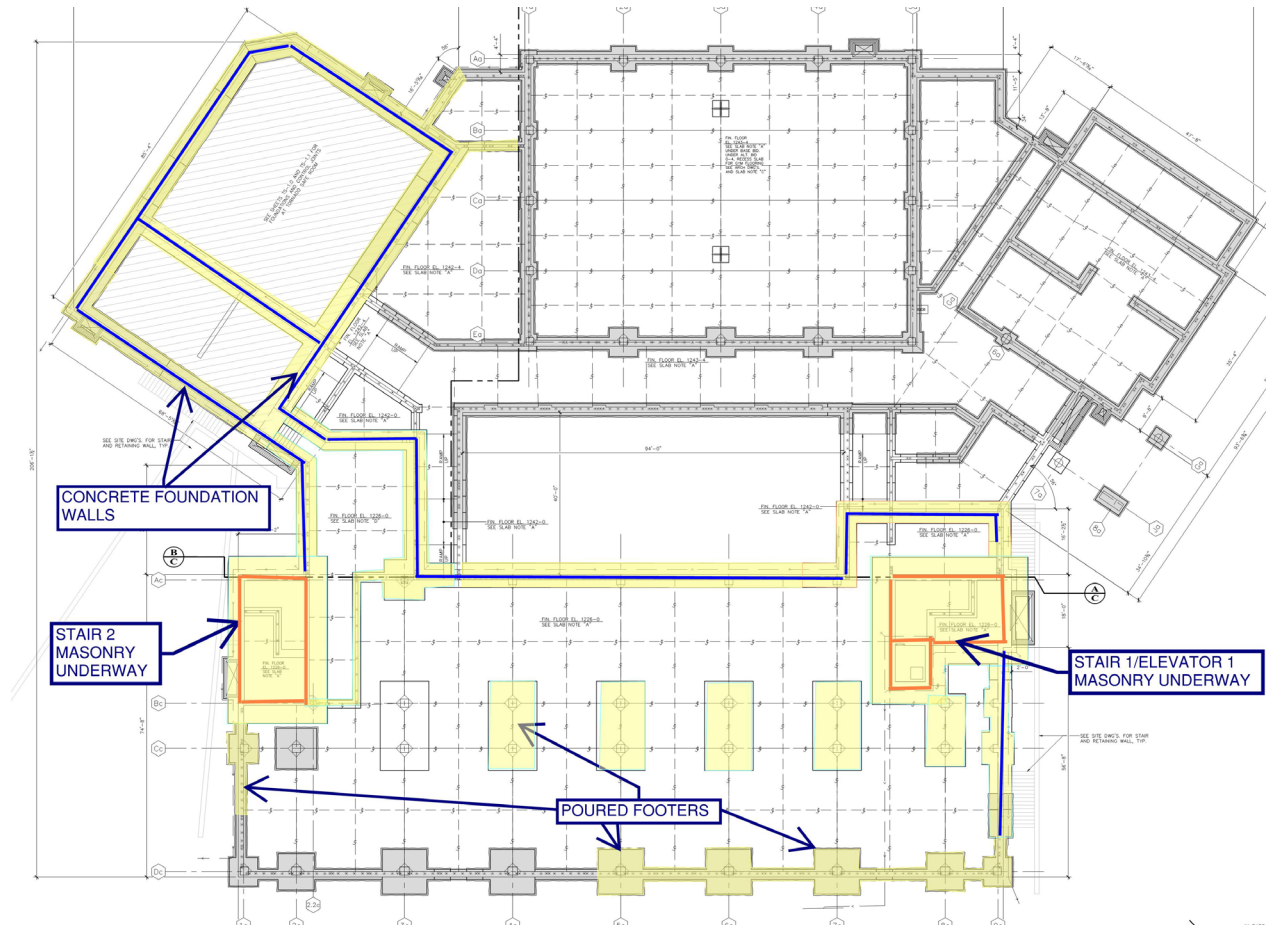

Mechanical Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Electrical Feeders – Installed & Protected



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC



Retention Tank Installation



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Safety Week – Standdown & Hilti Presentation



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

OVERALL PROGRESS

Upcoming Work:

- Complete forming and pouring foundations in Area C.
- Start foundations in Area A
- Finish MEP Coordination
- Complete masonry installation at Stairs 1 & 2.
- UG Plumbing & Electric in Area C
- Pour slab on grade in mech. room
- Storm line installation
- Backfill Foundation Walls
- Steel Erection to start in June

Project Schedule

- Mucci completed a project schedule update for May 16, 2025, and the project remains on schedule for substantial completion on August 14, 2026



Project Stats:

- Project is at 1 day with no recordable injury



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU

QUESTIONS?

