

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Foundation, Masonry, & Steel Progress

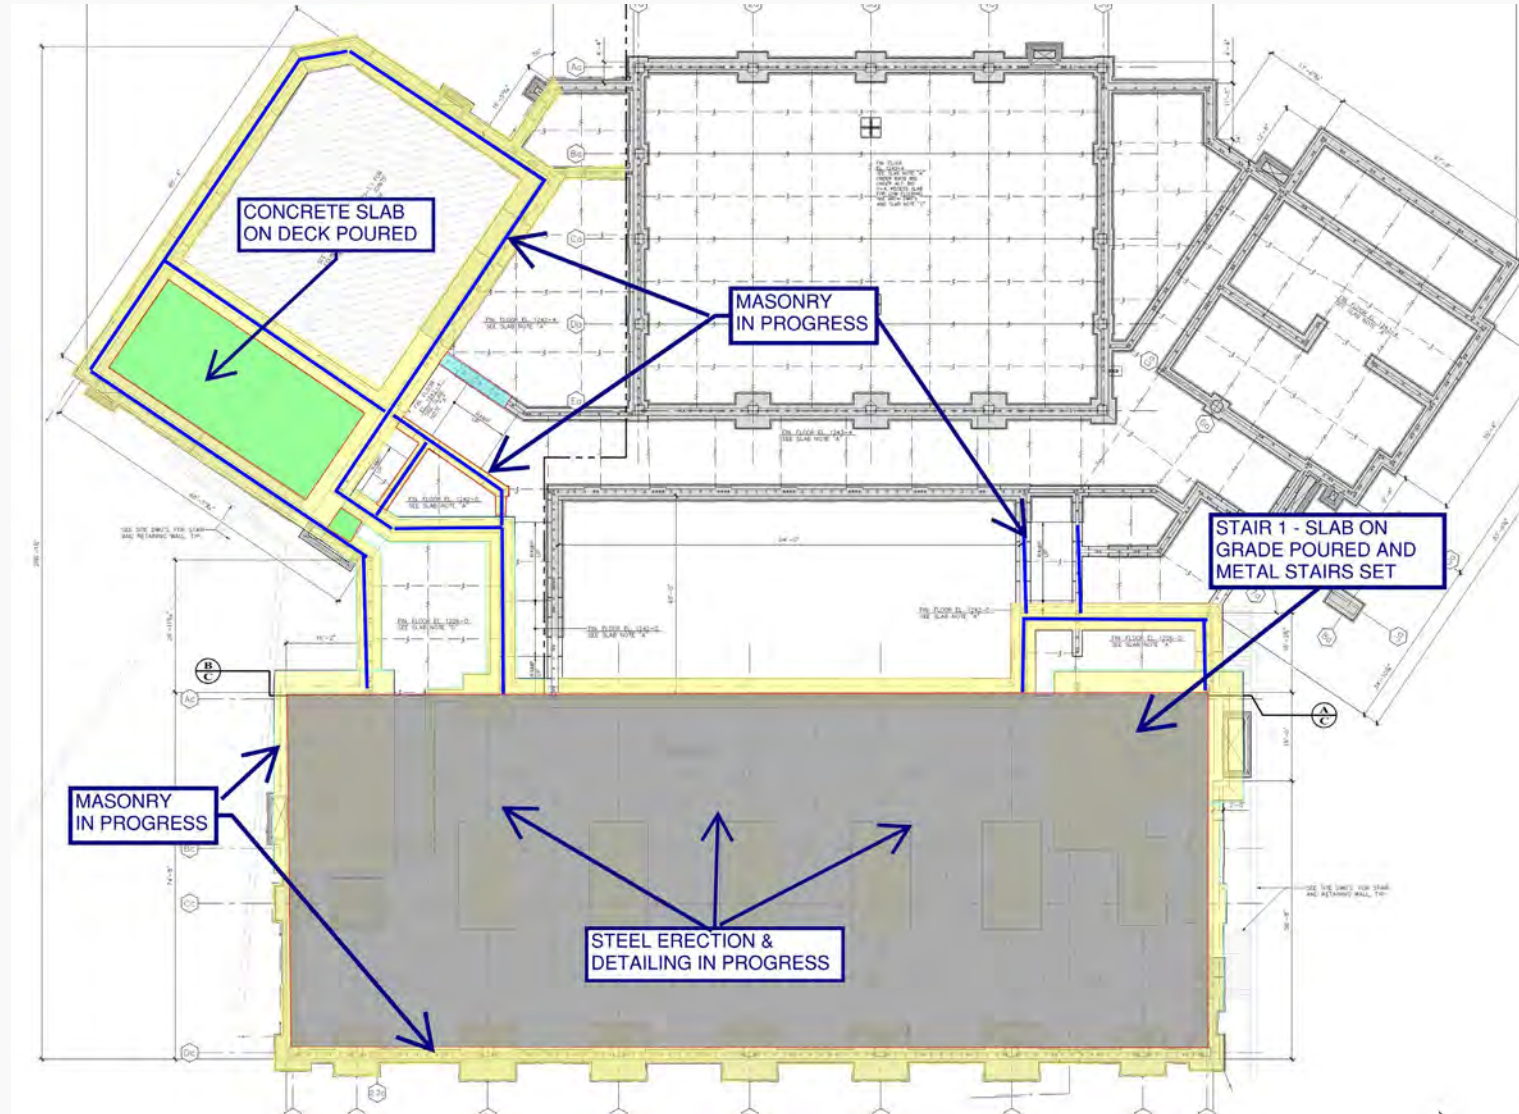

Foundations in Area B



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Stair 1 – Concrete Slab & Metal Stairs



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Walls



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Walls



Area C – Steel Erection



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Plumbing Underground Piping



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Electrical Underground Conduit




8/14/25 10:28:43 AM E



ARCHITECTS
ENGINEERS

Massaro
CM SERVICES, LLC

Backfill of Area C Concrete Wall

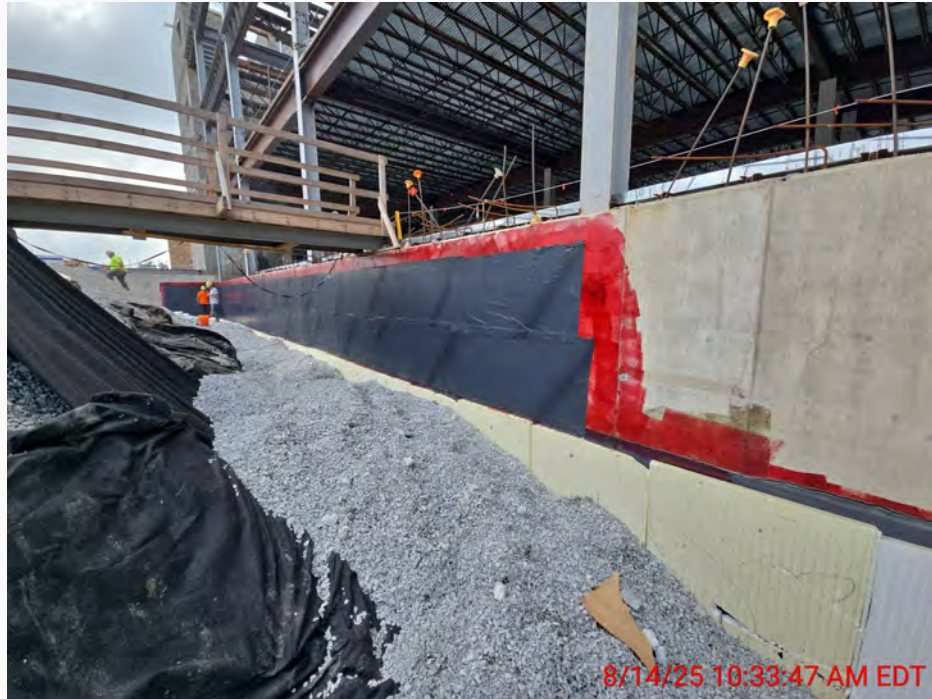

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Concrete Slab on Deck Above Mechanical Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

8/14/25 12:29:35 PM EDT

Final Mock Up Approval



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

OVERALL PROGRESS



Upcoming Work:

- Continue foundations in Area B
- Finish MEP Coordination
- Pour concrete at Stair 1 & Stair 2.
- Continue UG plumbing & electric
- Continue electrical feeder conduit installation
- Continue storm line installation
- Complete backfill foundation walls
- Complete steel detailing and deck placement at Area C
- Pour slabs on deck at Area C

Project Schedule

- Per Mucci's August 15th schedule update, the project remains on schedule for substantial completion on August 14, 2026



Project Stats:

- Project is at 69 days with no recordable injury



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU

QUESTIONS?

