

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE





HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

MEP Coordination & BIM Model Complete

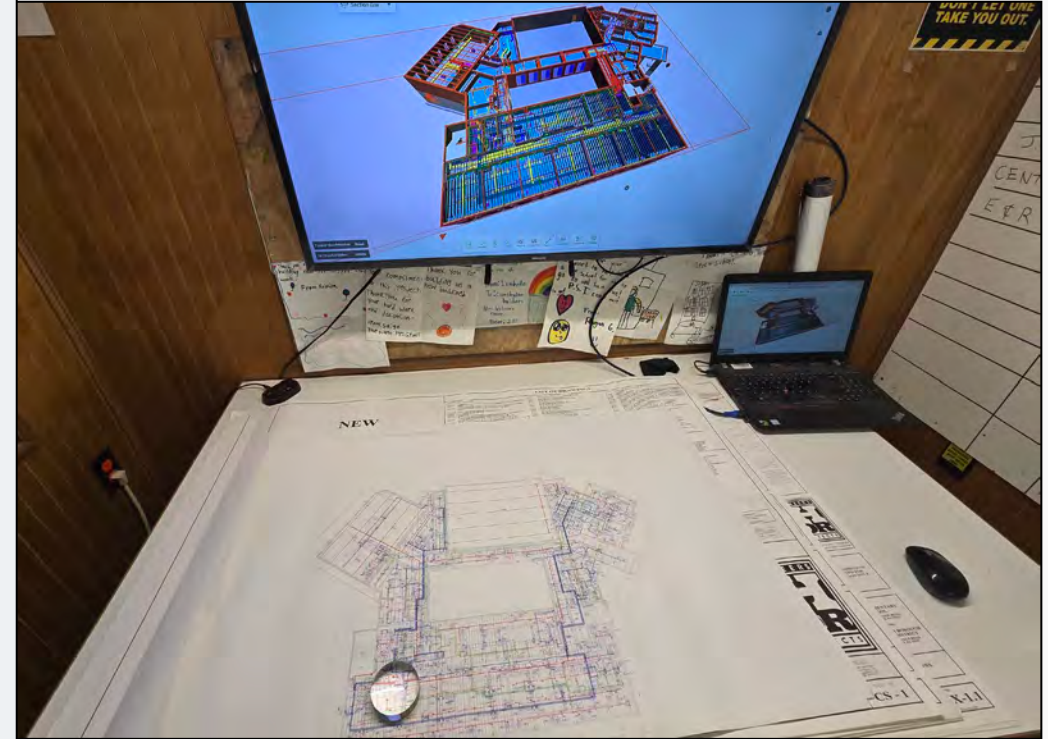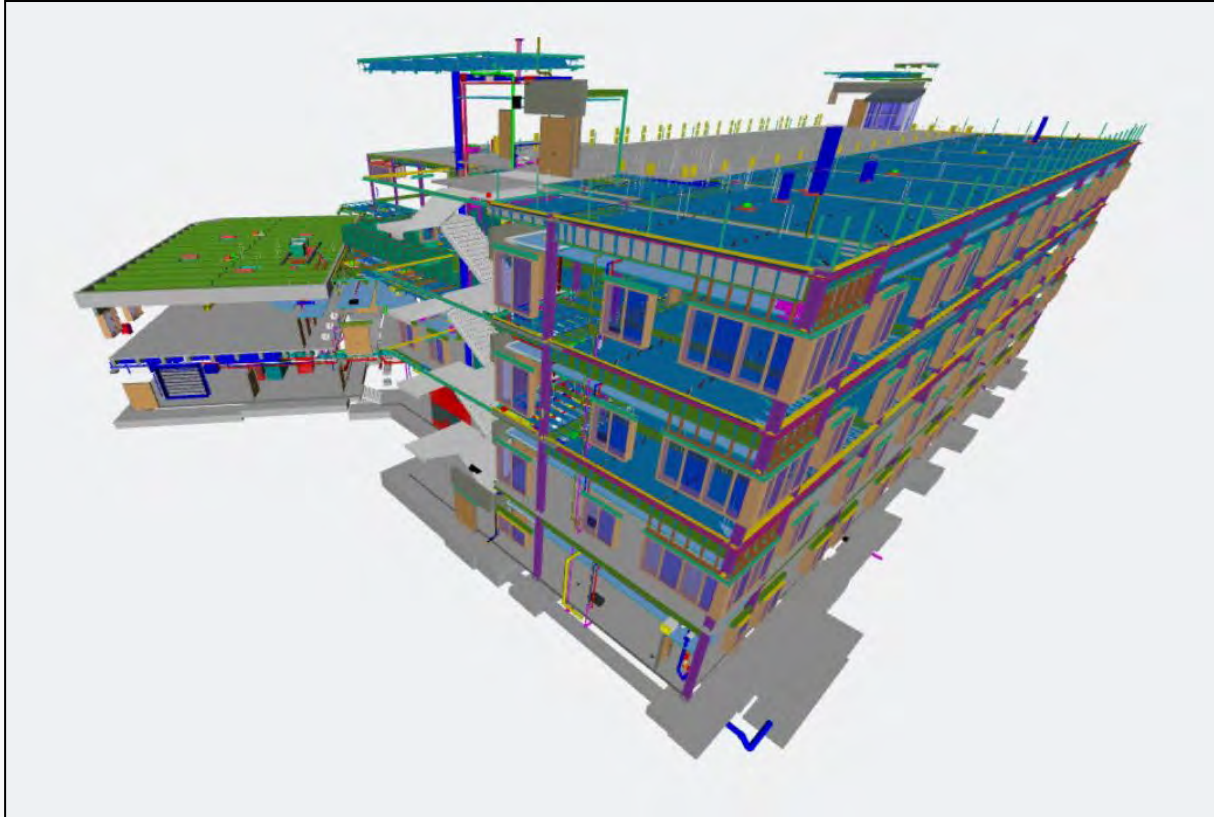


HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Foundation, Masonry, & Steel Progress

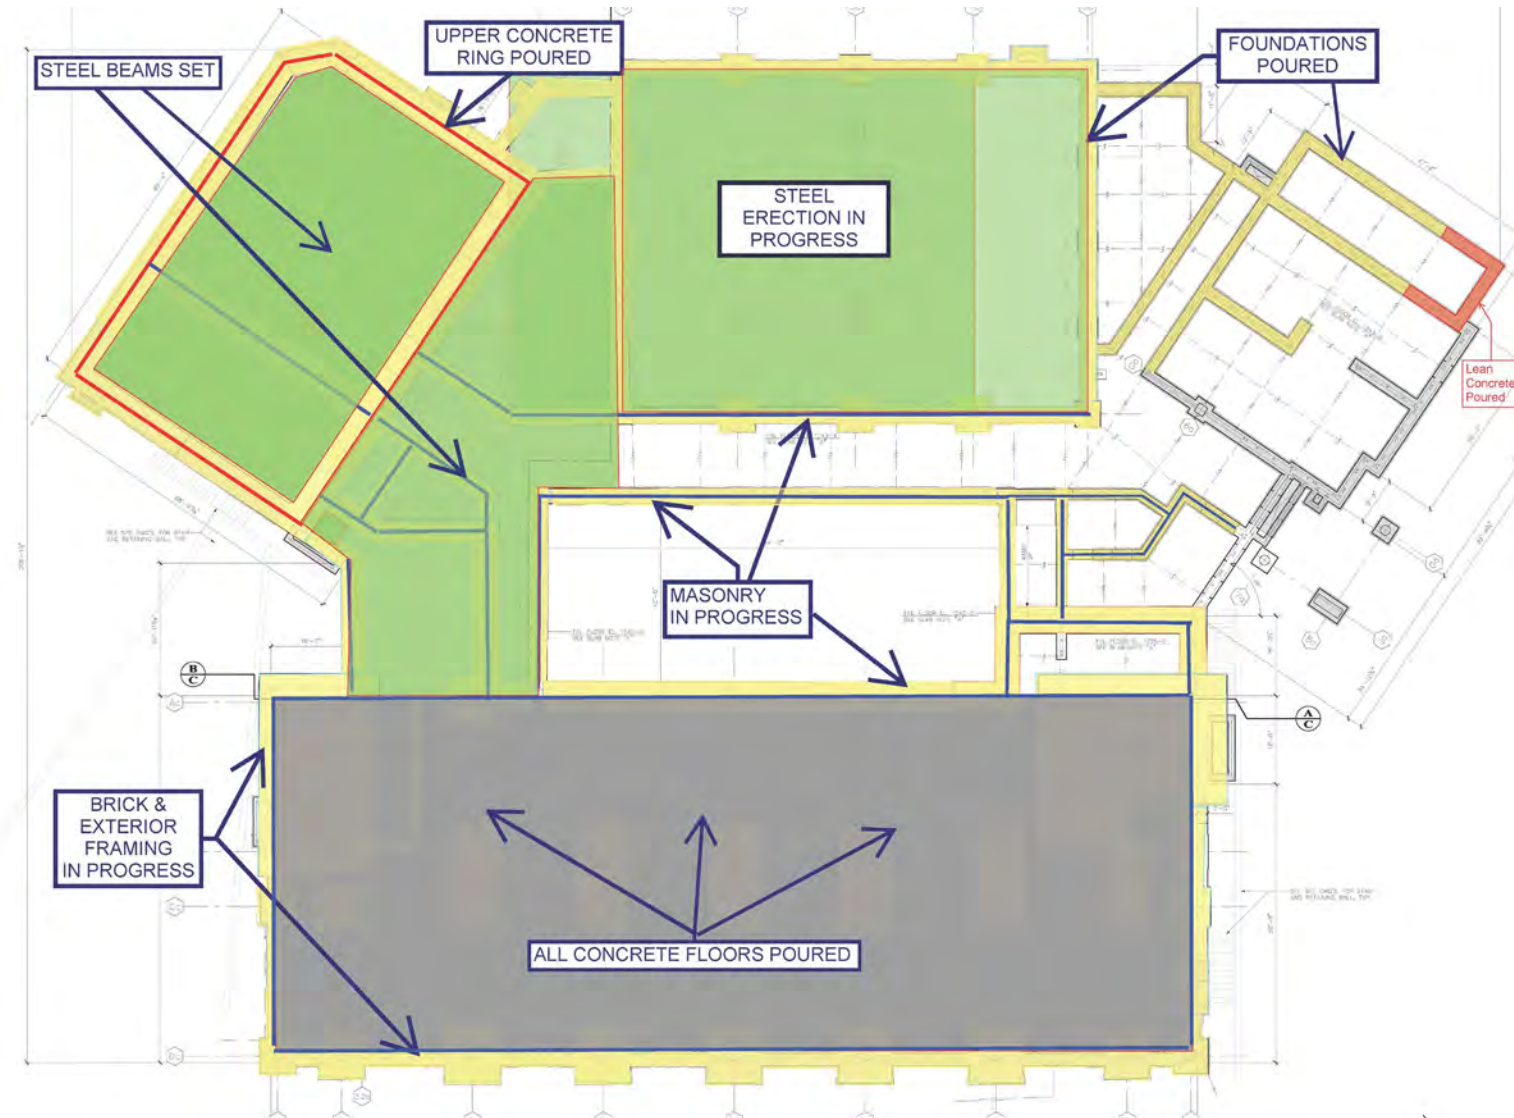

Foundations in Areas A



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area A – Foundation Progress



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Walls



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Masonry Walls



Steel Progress



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Ground Floor – Overall Progress




Framing is complete.

Rough In Progress:

- Plumbing - 75%
- Fire Protection – 99%
- Mechanical – 90%
- Electrical – 80%

Fireproofing – 95%

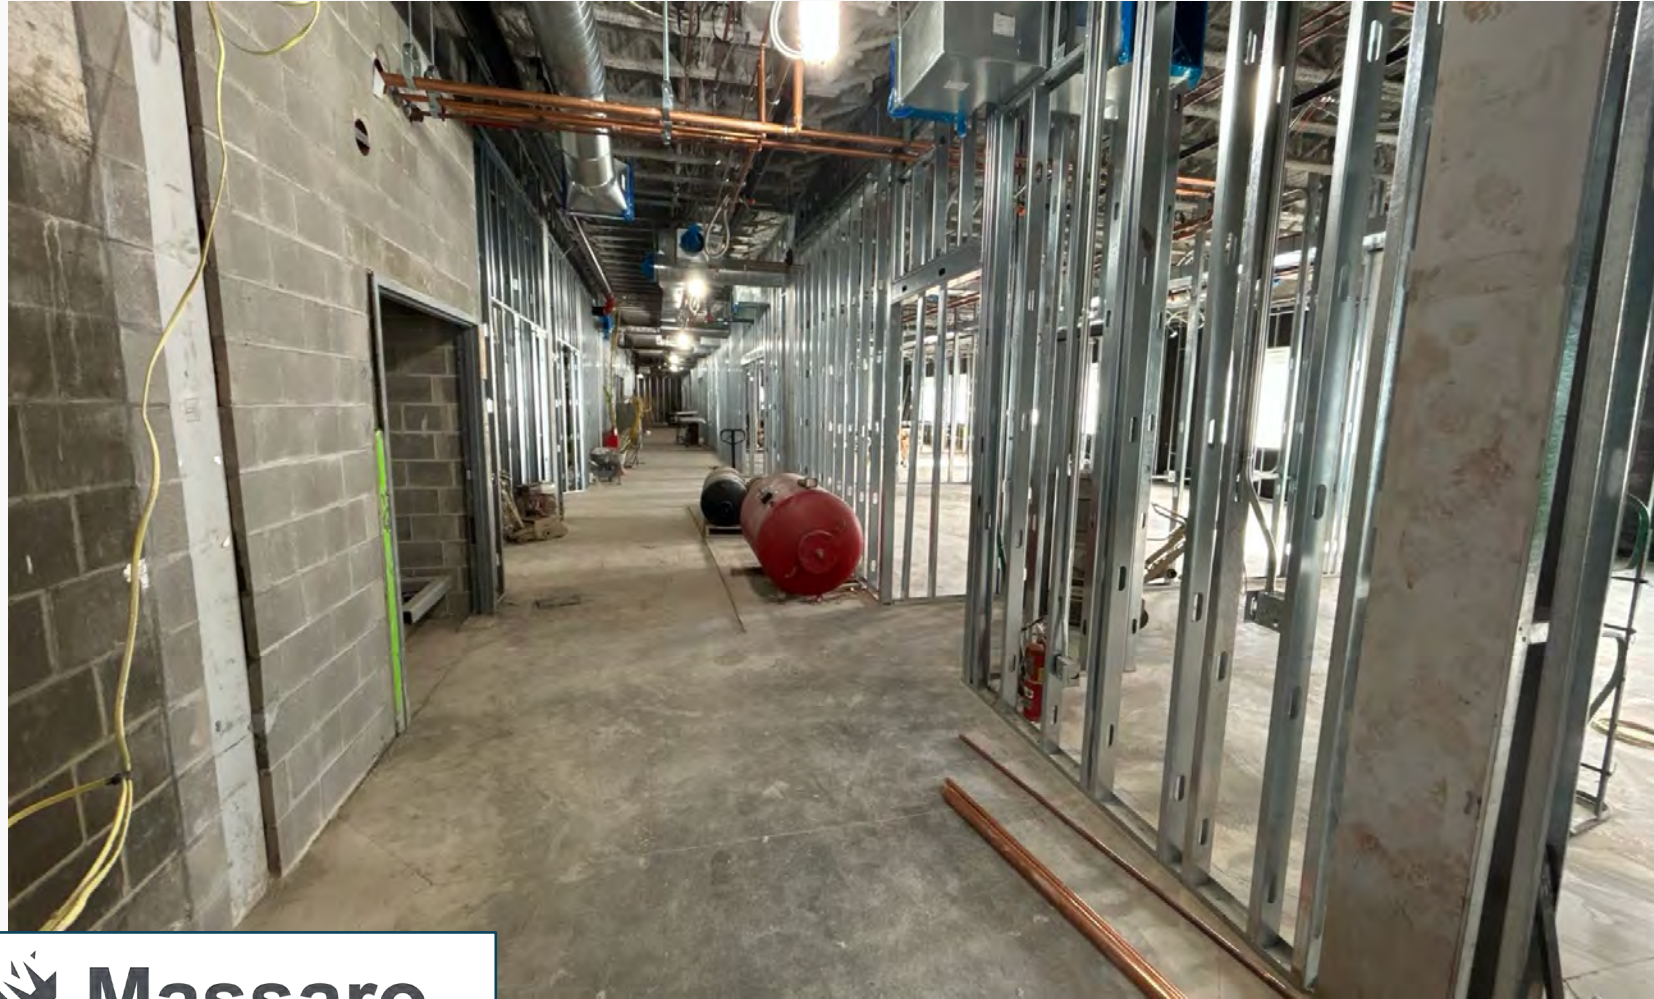

HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 1st Floor – Overall Progress



Framing is complete.

Rough In Progress:

- Plumbing - 50%
- Fire Protection – 75%
- Mechanical – 90%
- Electrical – 40%

Fireproofing – 95%



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 2nd Floor – Overall Progress



Framing is complete.

Rough In Progress:

- Plumbing - 15%
- Fire Protection – 95%
- Mechanical – 85%
- Electrical – 30%

Fireproofing – 95%



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 3rd Floor – Overall Progress




Framing is complete.

Rough In Progress:

- Plumbing - 10%
- Fire Protection – 88%
- Mechanical – 30%
- Electrical – 10%

Fireproofing – 99%

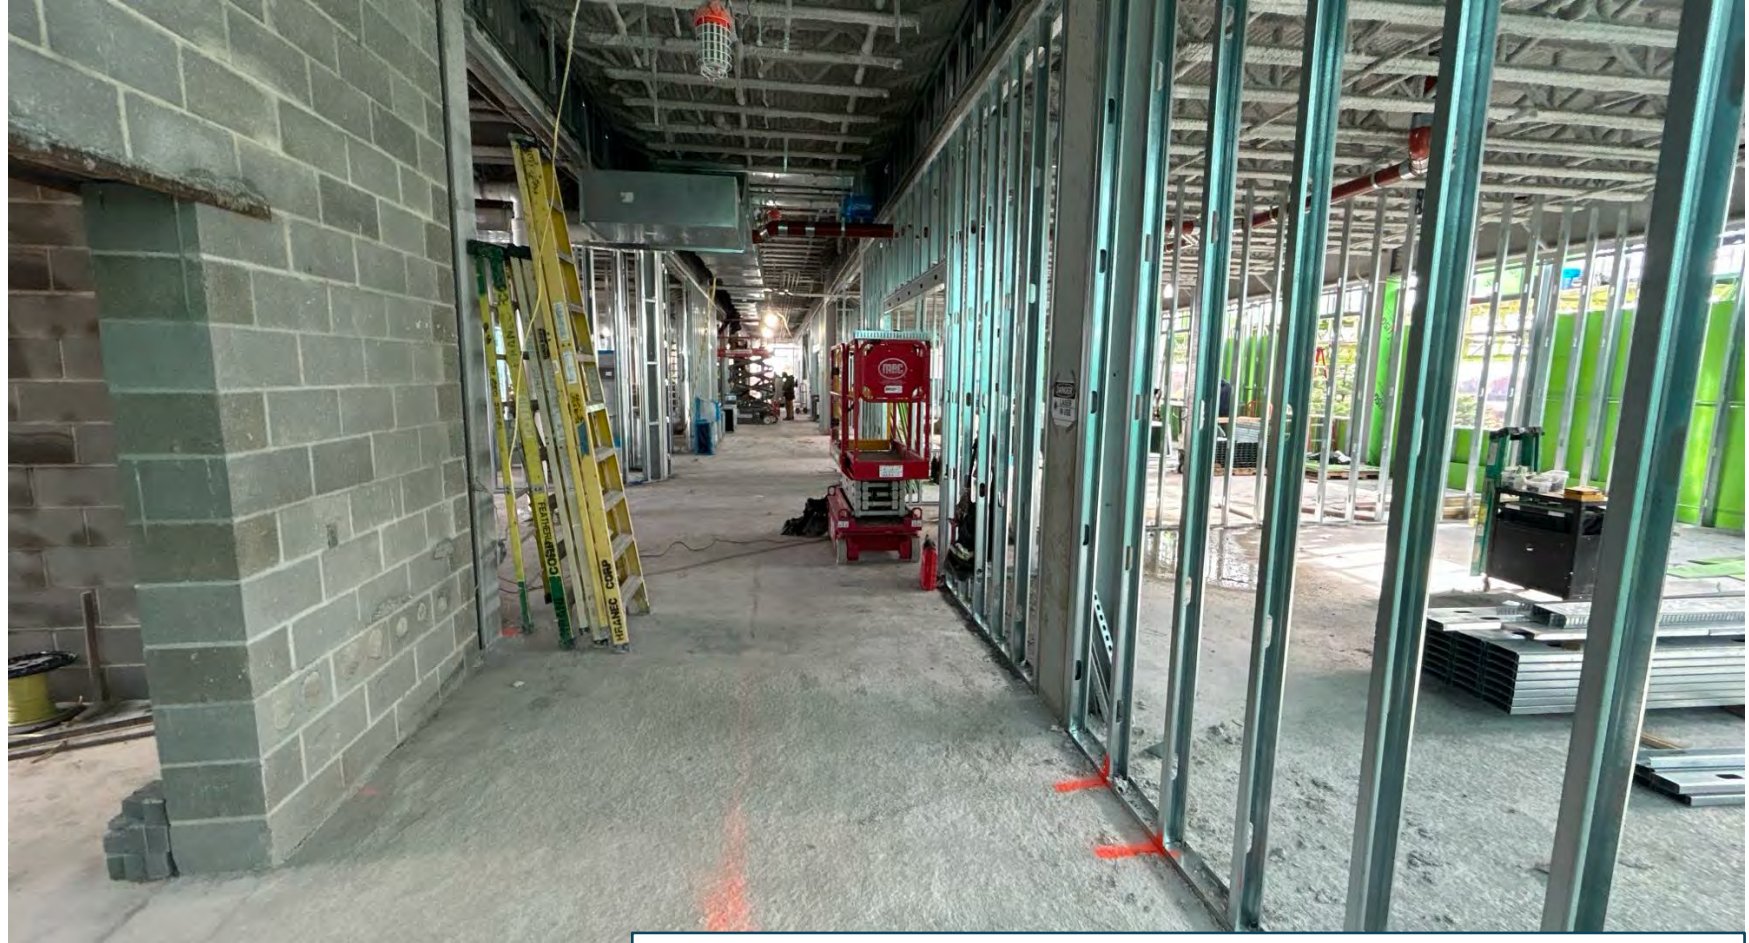

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Masonry Walls Complete & Roofing Started



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Exterior Sheathing



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area B – Switchgear Installation



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – UG Plumbing at Kitchen



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

HS & MS Students Visit Site



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

OVERALL PROGRESS



Upcoming Work:

- Continue foundations in Areas A
- Complete steel erection at gym
- Continue UG plumbing & electric
- Complete fireproofing Area C
- Continue Mechanical, Electrical, and Plumbing Rough In at Area C
- Continue exterior sheathing at Area C
- Roofing at Area C
- Area B rough ins
- Continue block and brick installation
- Participation in MS Career Day – 11/21

Project Schedule

- Per Mucci's November 14th schedule update, the project remains on schedule for substantial completion on August 14, 2026



Project Stats:

- Project is at 1 day with no recordable injury



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU

QUESTIONS?

