

Brentwood Borough School District

New Elementary School



Construction Update
February 24, 2024



HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Foundation Wall at Area C



HHSDR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Forming and Rebar for Stair 1/Elevator 1 Pad at Area C



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Concrete Pour at Stair 1/Elevator 1 Pad at Area C



HHSDR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Stair 1/Elevator 1 Pad at Area C

Pour Complete and Blankets Placed



HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Forms Stripped from Foundation Walls at Storm Shelter




HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Pouring Lean Concrete & Foundations

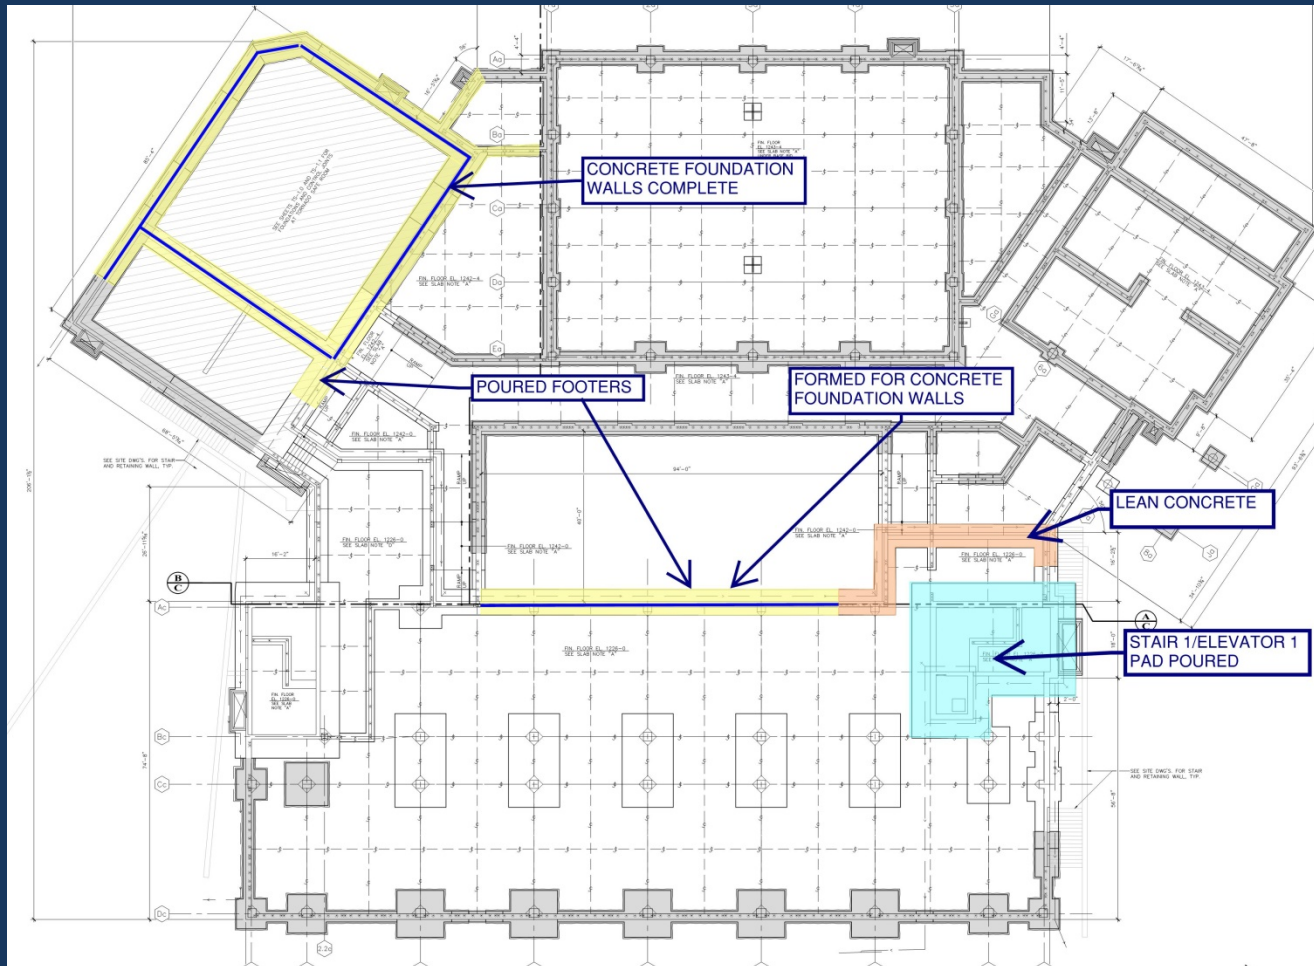

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Placement of Lagging at Retaining Walls



HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Placement of Lagging for Retaining Walls



HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Placement of Lagging for Retaining Walls



HHSDR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Placement of Lagging for Retaining Walls



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Massaro Safety Committee Site Visit



HHSDR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC

Overall Progress

Upcoming Work:

- Temporary electric connection by Duquesne Light
- Continue forming and pouring foundations.
- Finish lagging installation at retaining walls
- Installation of water meter vault and water service to site.
- Continue MEP Coordination
- Stair 1 masonry to start mid-March

Project Schedule

- Project is on schedule for substantial completion on August 14, 2026



Project Stats:

- Project is at 93 days with no recordable injury



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Questions



HHS DR
ARCHITECTS
ENGINEERS



 **Massaro**
CM SERVICES, LLC
