




School Board – School Design Update ***South Fayette Twp School District***

October 22, 2024



IES Addition – Site Plan

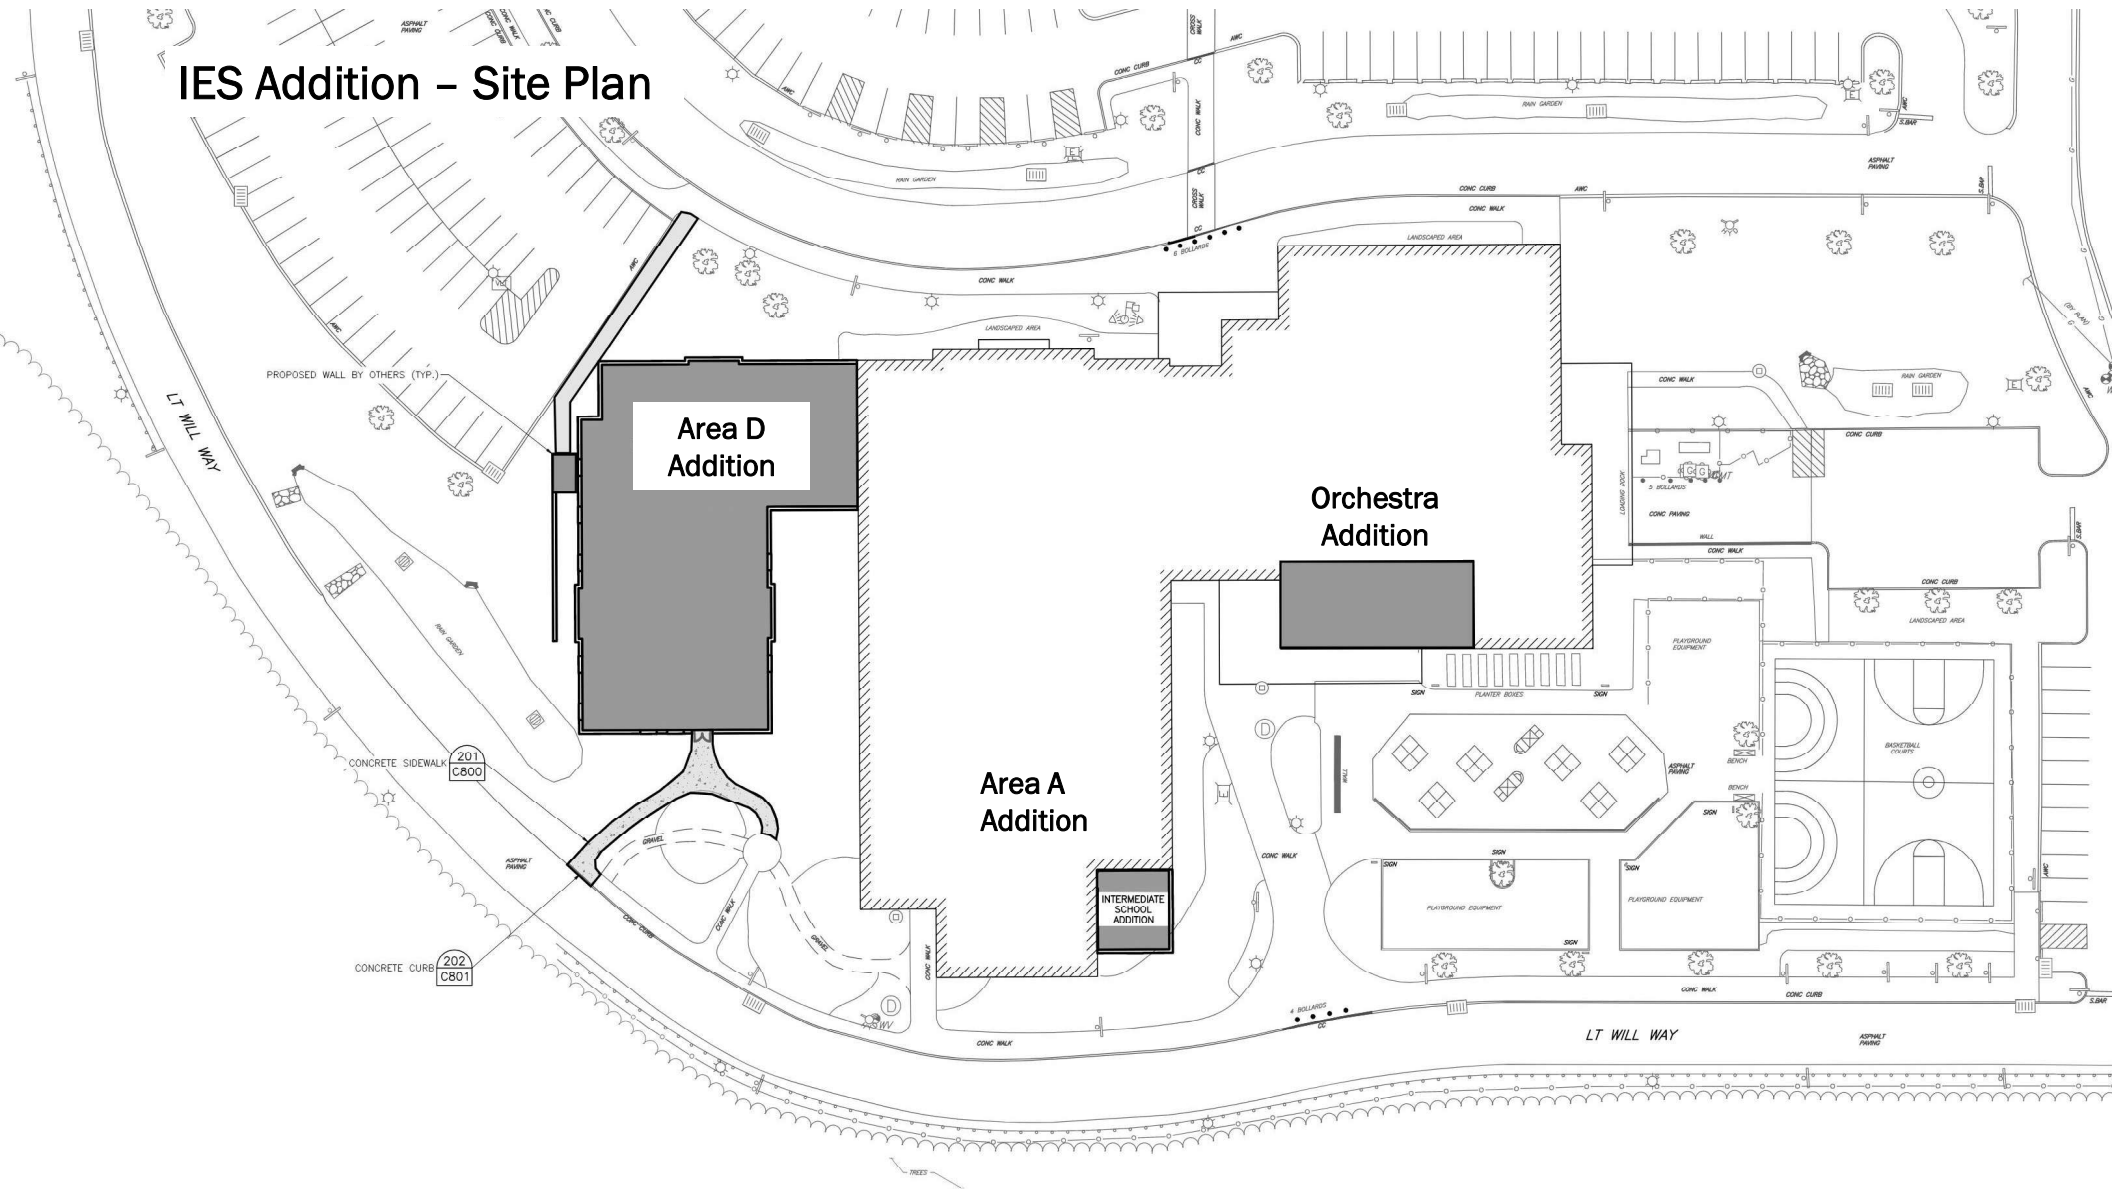

IS Addition – Overall Plan

Ground Floor
3rd GRADE



IS Addition – Overall Plan


First Floor 4th GRADE



IS Addition – Overall Plan

Second Floor

5th GRADE

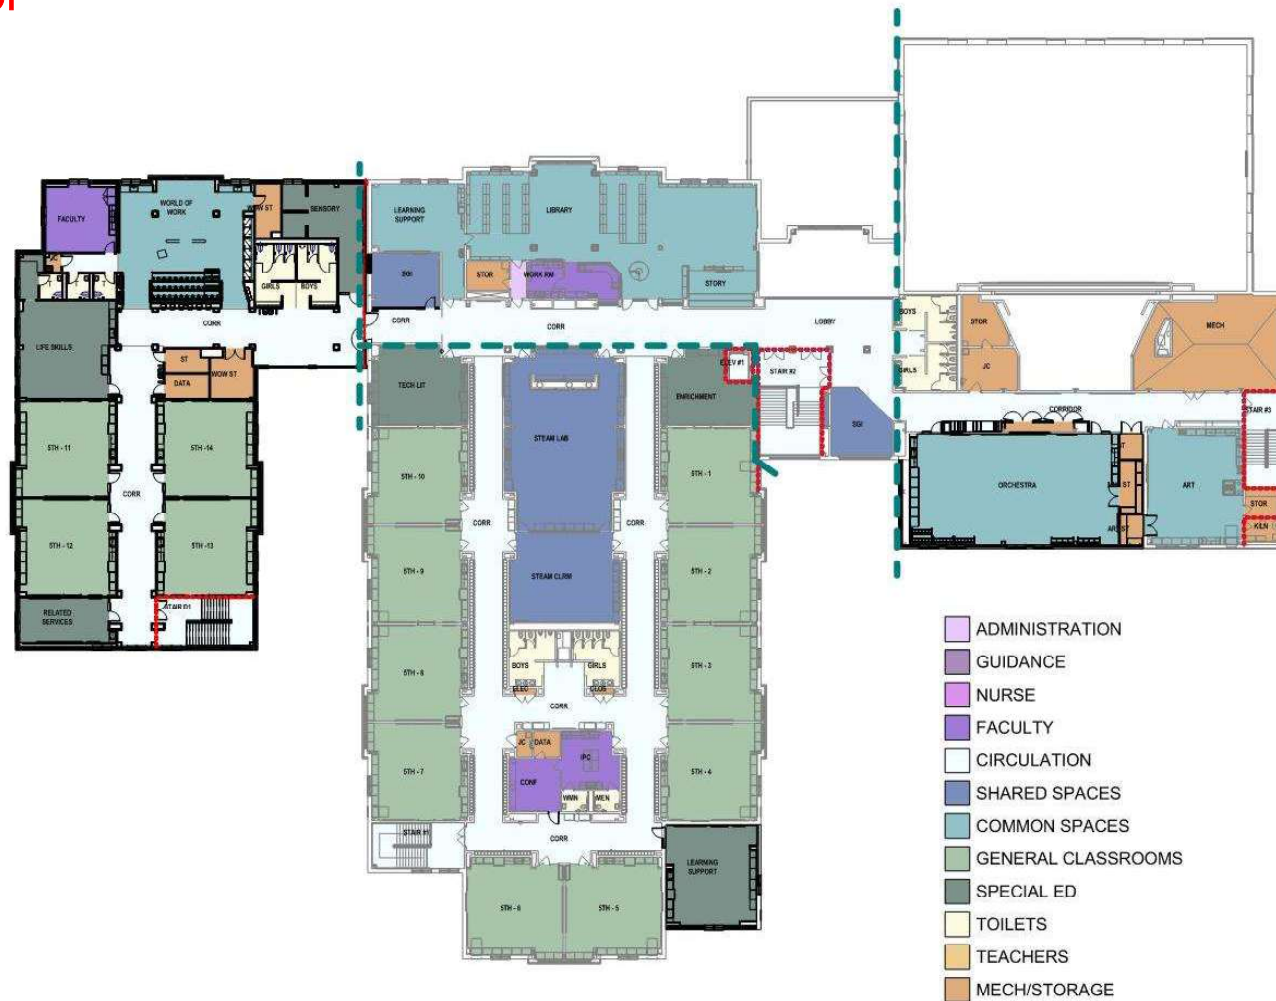


Intermediate School Addition – Front Exterior View



Intermediate School Additions – South Exterior View



IS Addition Final Design Reviews with Staff

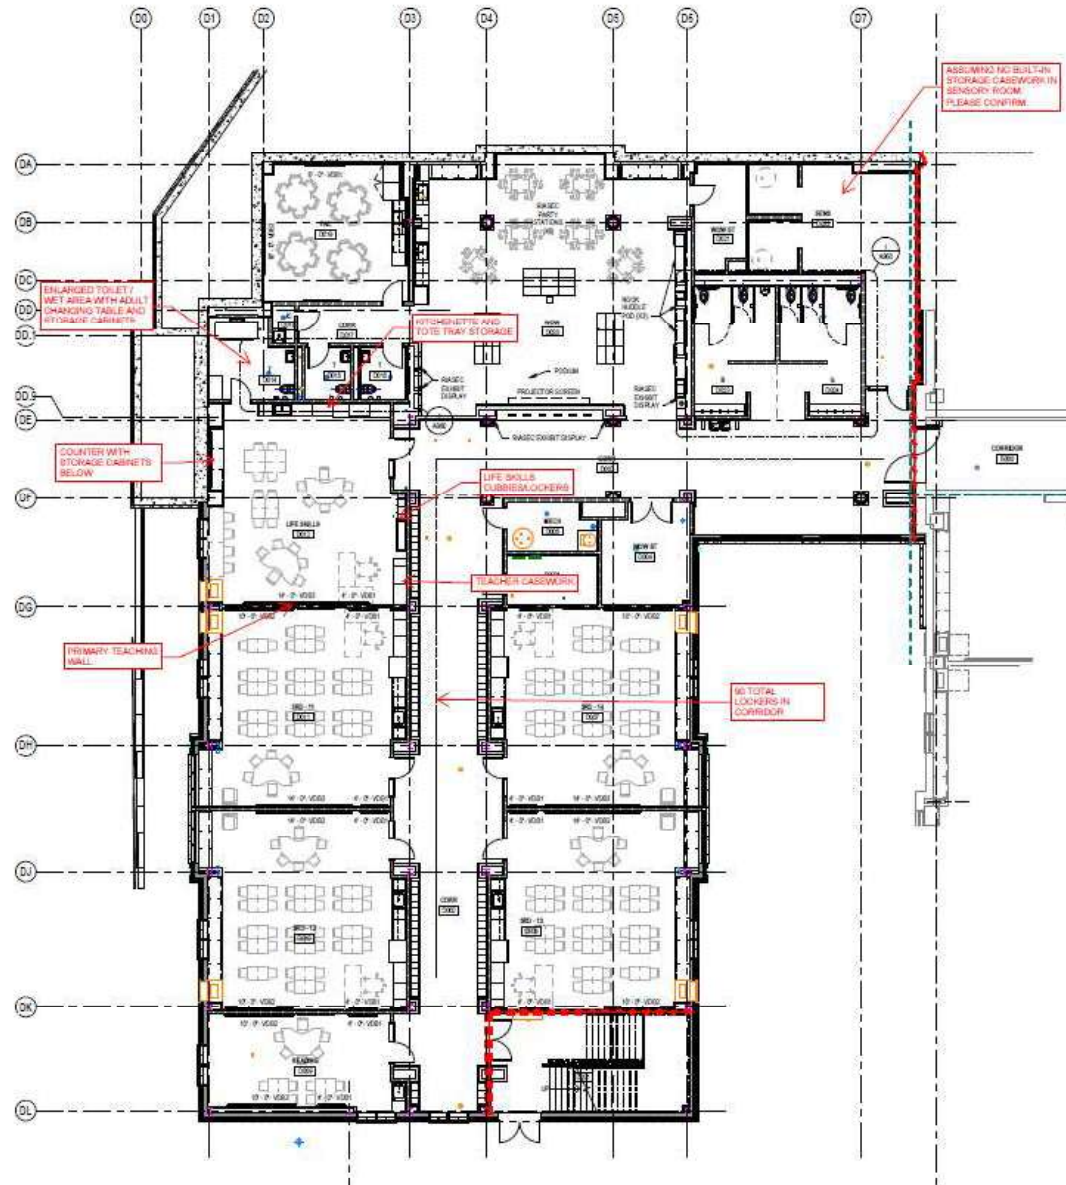

Project Activities

1. Intermediate School Additions (Construction Document Phase)

1. 90% construction documents completion due Friday. Internal coordination reviews begin next week.
2. We are currently in the final design verification time with the Administration and Staff. Recent design decision to include Alternates for Cell Phone Booster systems at all schools.
3. On track to complete construction documents by end of November.
4. Final document review and coordination by DRAW and PJ Dick in December.
5. Dec 2nd, submission to Municipality for final Code and Permit Approval.
6. Out for public bidding beginning of January 2025.

2. New Primary School (Schematic Design Phase)

1. Completed first design meeting of Administration Core Team and K-2 Grade Level Teaching Leads. Monthly meetings are planned moving forward.
2. Preparation of preliminary Geotechnical investigation proposal in progress. Civil Engineering response to Board for November review/approval.
3. Upcoming educational department meetings planned prior to years-end.

3. New Transportation / Maintenance Facility (Schematic Design Phase)

1. Land Surveying begins tomorrow (Oct 23rd).
2. Schematic Site Design & Building Schematic planning Options to be complete by end of October.
