

BRENTWOOD BOROUGH SCHOOL DISTRICT

NEW ELEMENTARY SCHOOL MONTHLY PROJECT UPDATE



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Bar Joists & Roof Decking Installed



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Admin Waiting Area



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A



Principal Offices & Storage

Conference Room, Kitchenette & Restrooms



Progress in Area A – Security Office & Health Suite



Security Office



Health Suite

Progress in Area A – Gym



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – Gym



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A – IDF, Storage & Restrooms



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area A



- CMU - 65%
- Structural Steel – 95%
- Roofing Material will be delivered Thursday, 5/21/2026 for the admin area.
- Concrete Slab on Grade pours are ongoing
- Roof Drains will start this week.



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Courtyard




HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area B – Storm Shelter / Cafeteria

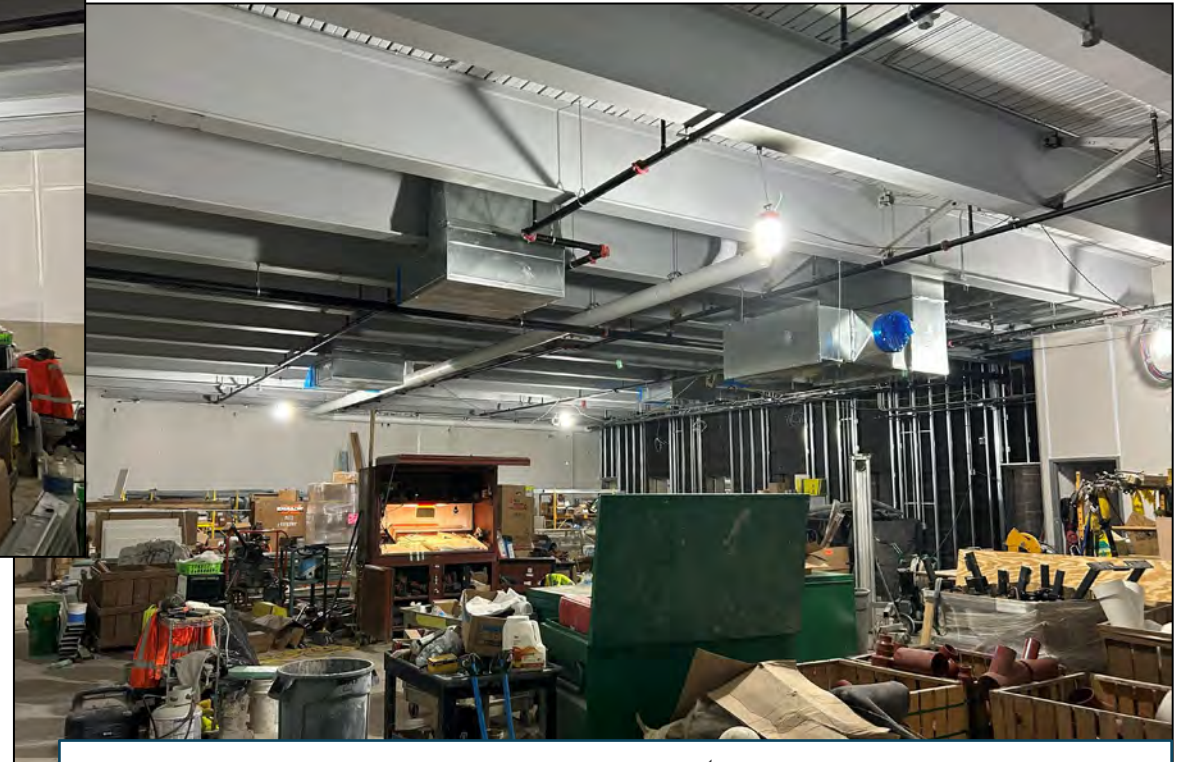

- Drywall – 85%
- MEP Rough ins – 95%




HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Progress in Area B – Kitchen

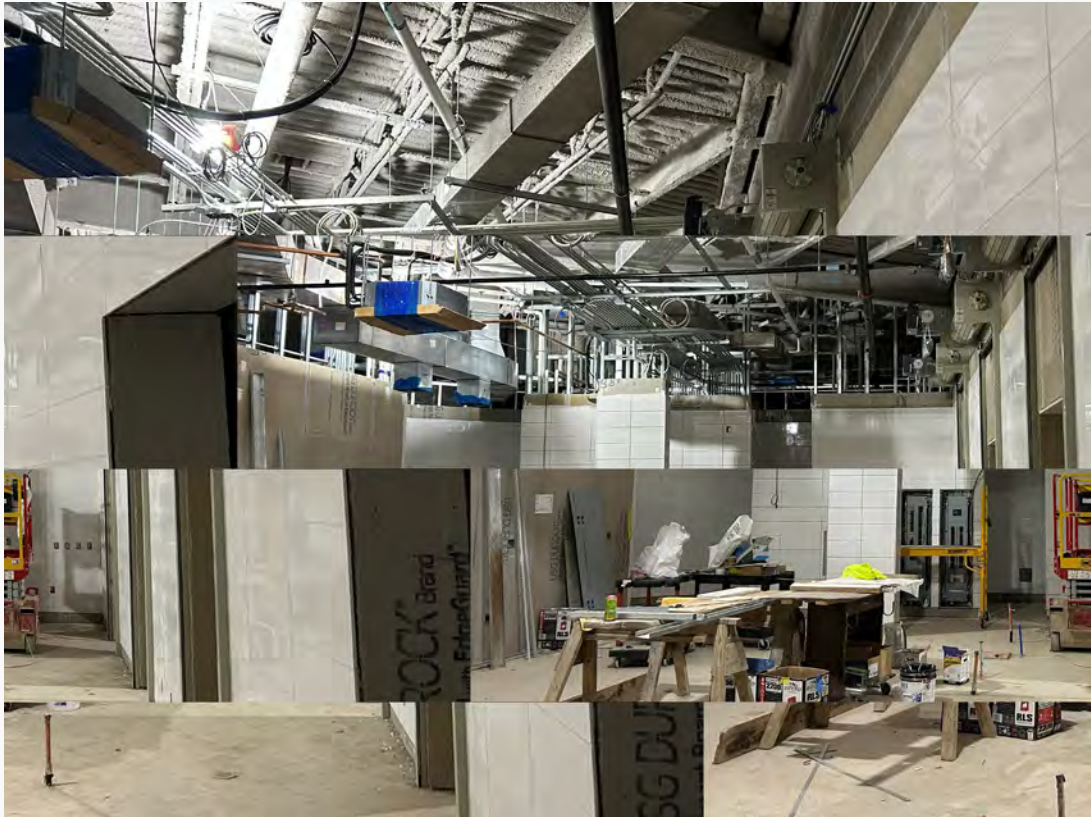

HHS DR
ARCHITECTS
ENGINEERS




Massaro
CM SERVICES, LLC

Progress in Area B - Kitchen



- MEP Rough Ins – 100%
- Ceramic Tile – 95%
- Kitchen Hood Installation Scheduled for tomorrow – 5/19/2026

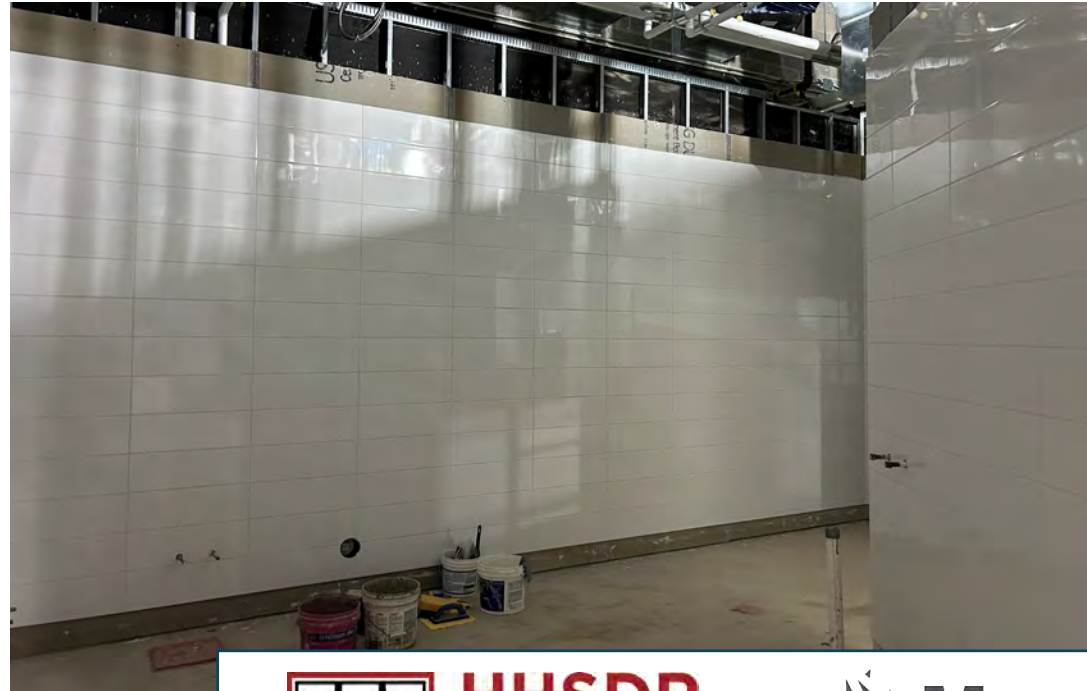

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area B Ground Floor – Mechanical Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area B Ground Floor – Mechanical Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area B Ground Floor – Mechanical Room



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor



Art Classroom

Kiln & Storage Room



Area C Ground Floor – Corner Classroom




HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Restrooms

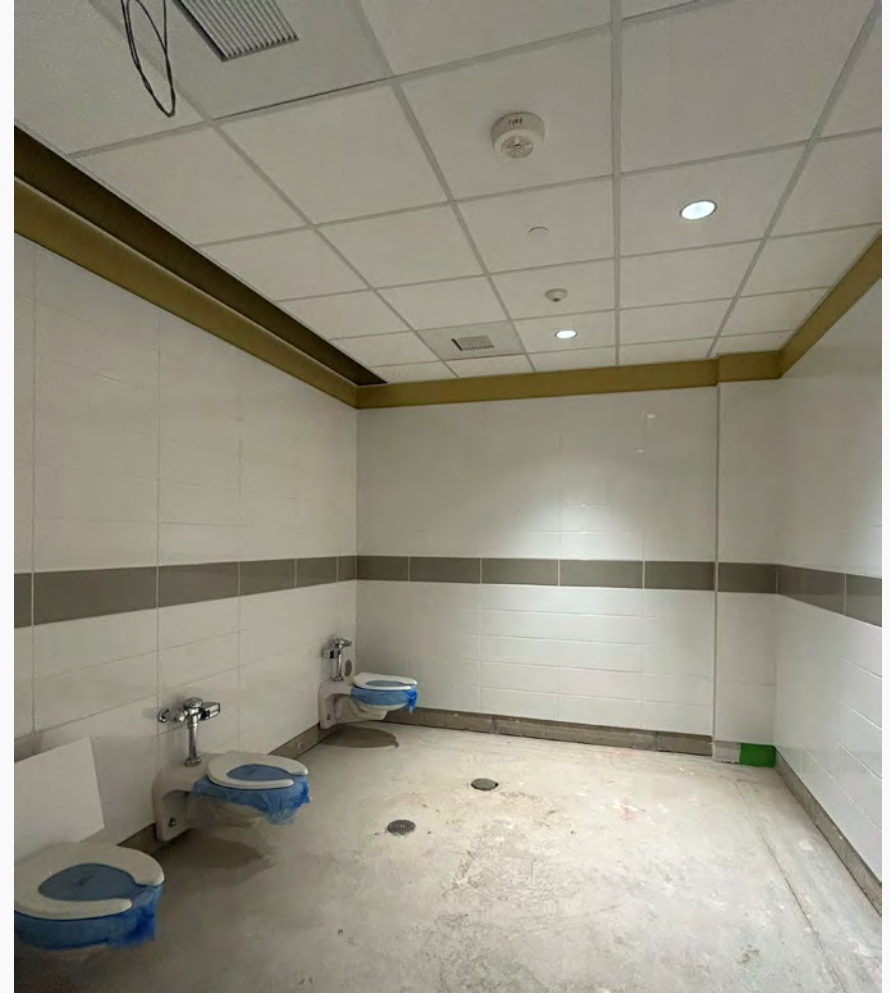


HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – MDF & Storage

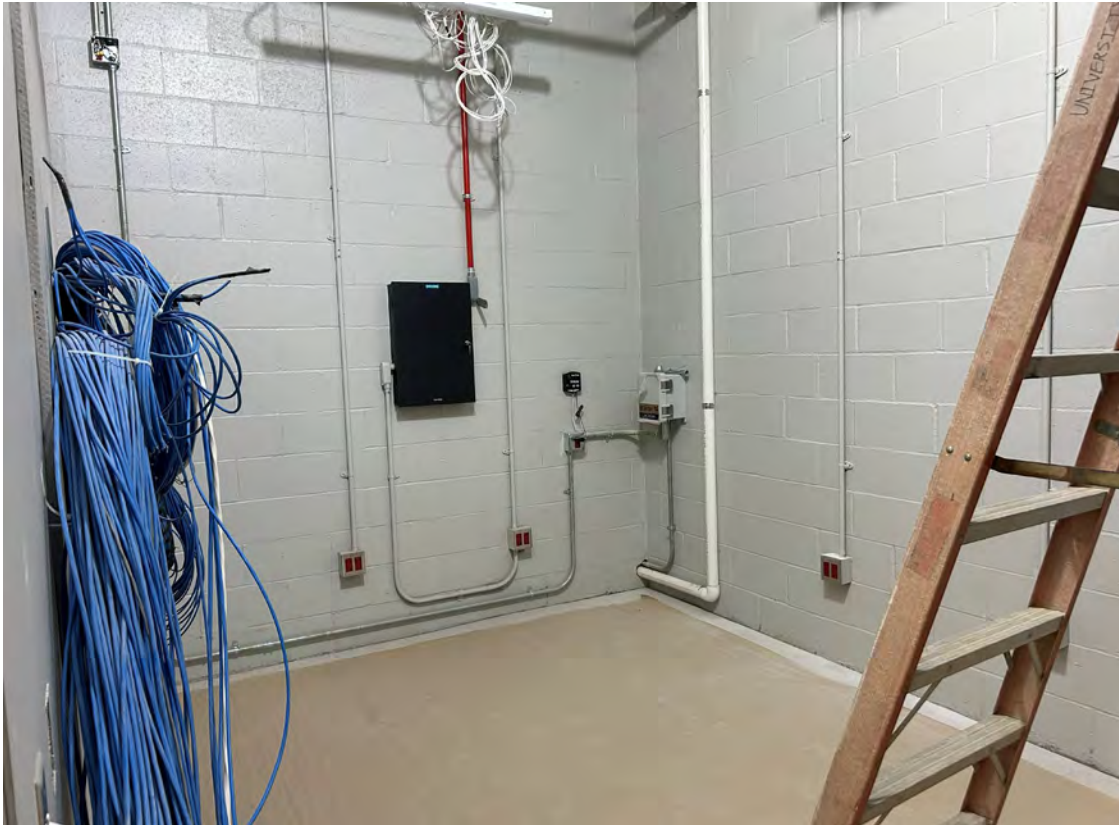

HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C Ground Floor – Doors Ready for Installation



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Ground Floor – Overall Progress



Painting & Ceramic Tile - 100%

Ceilings – 90%

Light Fixtures – 100%

Flooring – 45%

Casework to be delivered this week



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Title 1



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Life Skills



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Restrooms



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Media Center



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 1st Floor – Learning Support



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – 1st Floor – Overall Progress



Drywall – 100%

Painting & Ceramic Tile – 95%

Ceilings – 50%

Plumbing Fixtures – 100%

Light Fixtures - 75%



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Typical Classroom





HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 2nd Floor – Restrooms

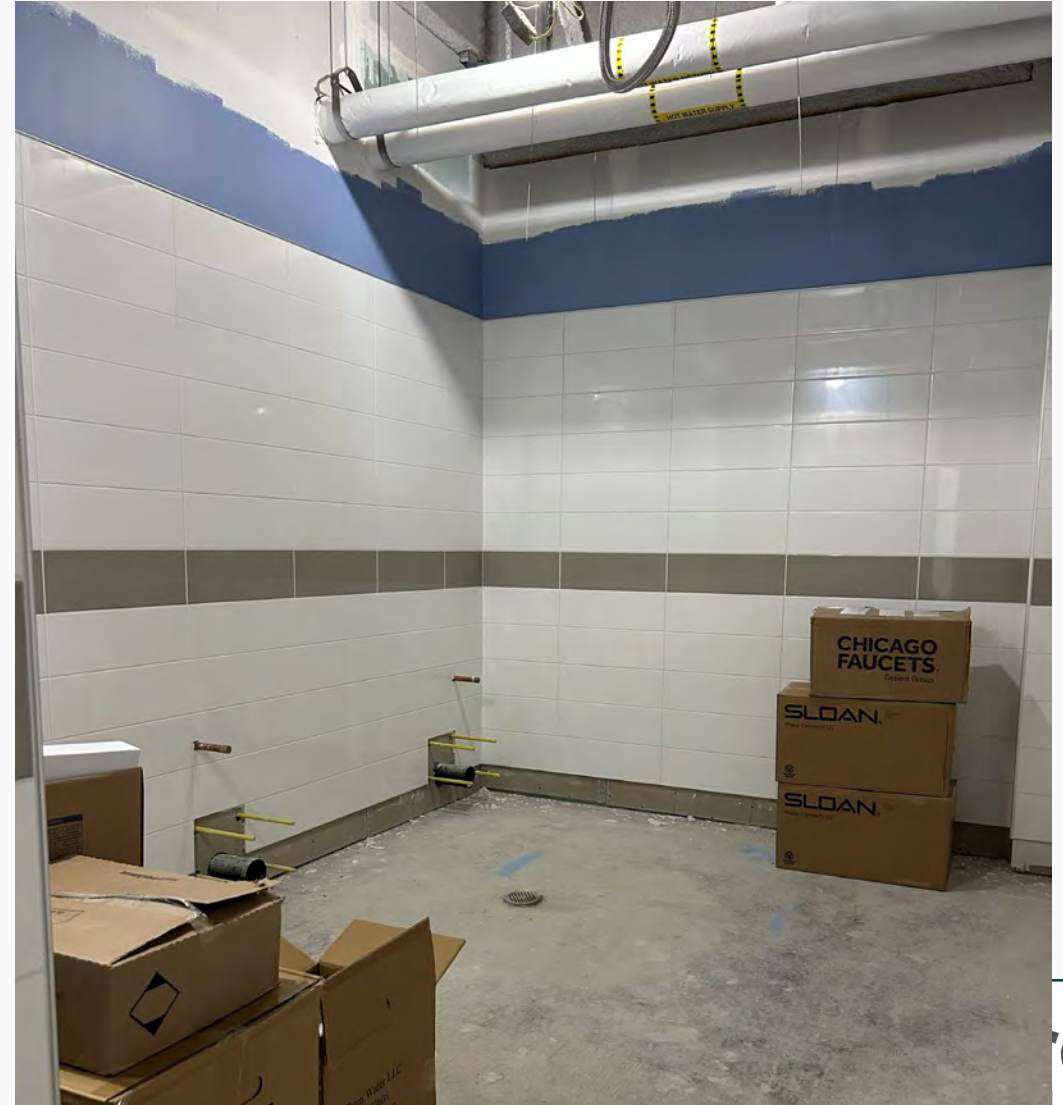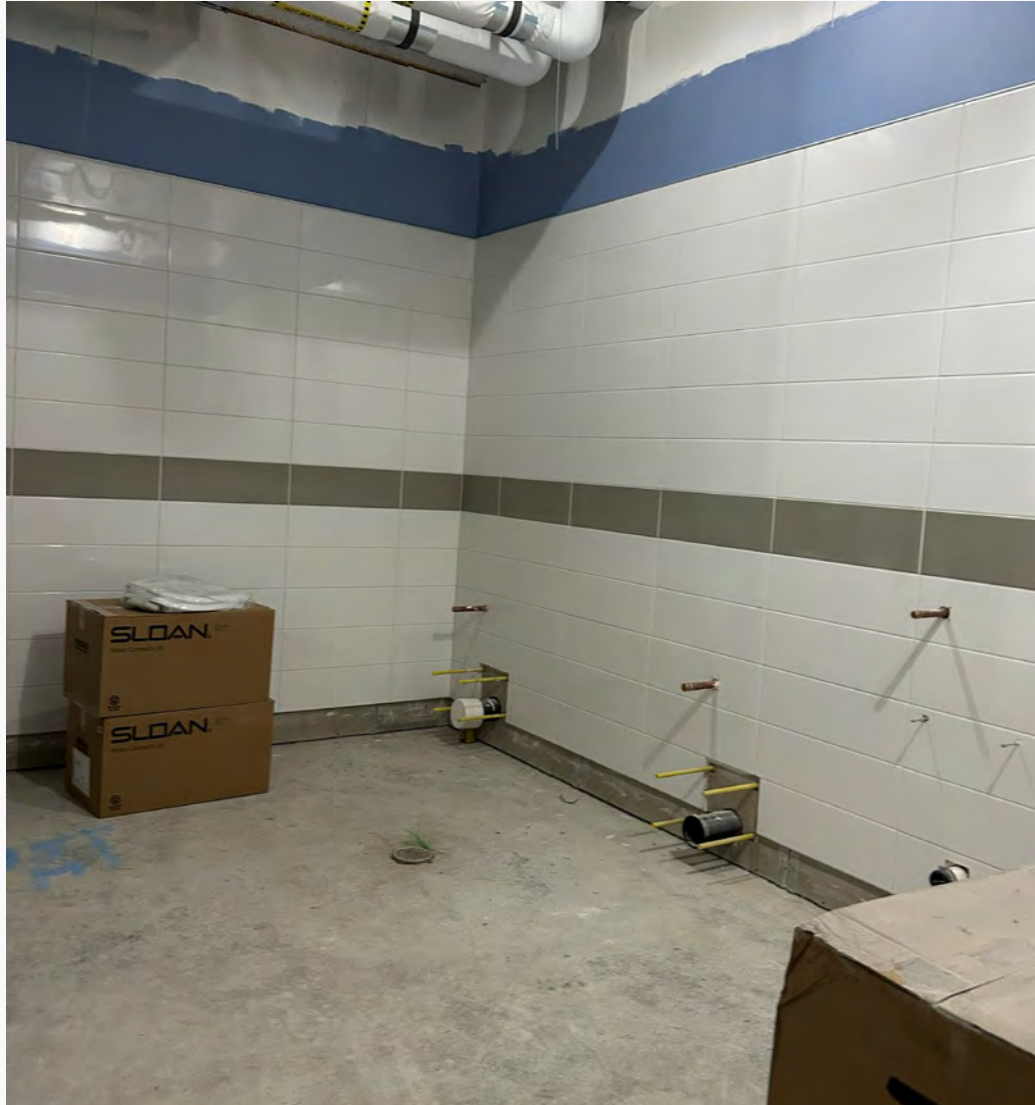

Area C – 2nd Floor – Overall Progress



Drywall Progress – 100%

Painting & Ceramic Tile – 90%

Ceilings – 25%



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 3rd Floor – Typical Classroom



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C 3rd Floor – Tile in Restrooms



Area C – 3rd Floor – Overall Progress



Drywall - 100%

Painting & Ceramic Tile – 15%

Window Installation Ongoing



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Roof



CMU Completed

Starting playground
surfacing soon



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC




Area C – Roof – Restrooms



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

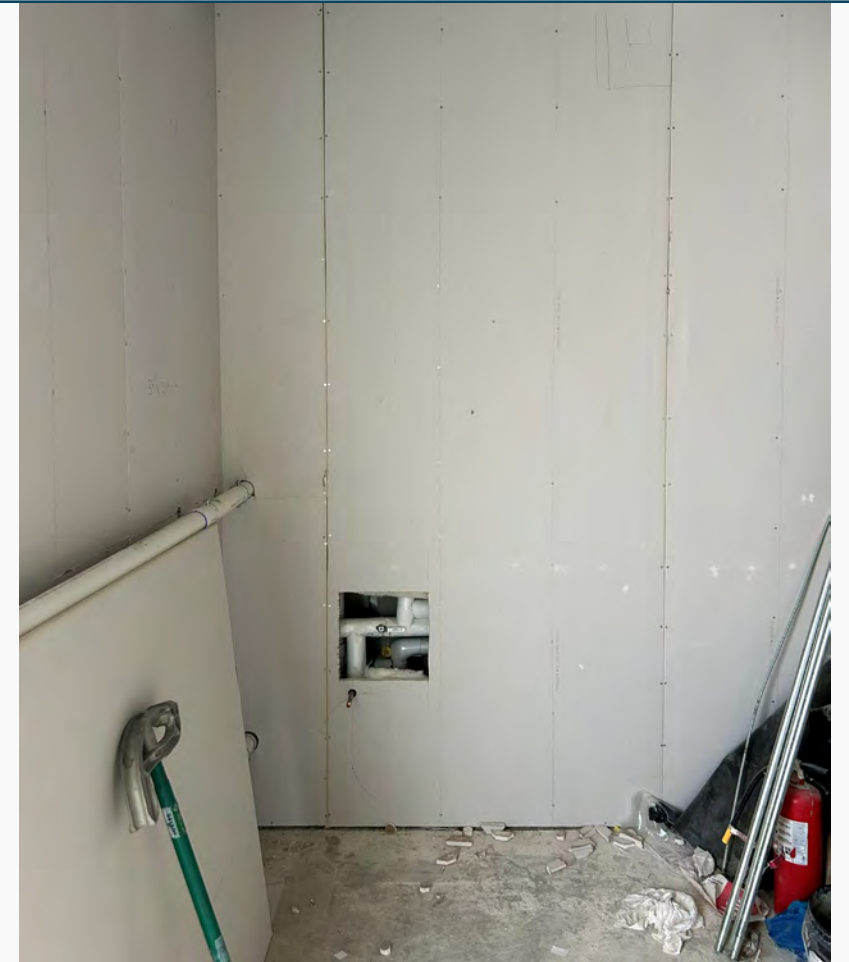

Area C – Stairwell 1



	HHS DR ARCHITECTS ENGINEERS		Massaro CM SERVICES, LLC
--	--	--	------------------------------------

Area C – Brick Progress – South Elevation Complete



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Brick Progress – North Elevation



90% Complete

HHS DR
ARCHITECTS
ENGINEERS

Massaro
CM SERVICES, LLC

Area C – Brick Progress – West Elevation



100% Complete



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Area C – Brick Progress – East Elevation



HHSDR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC



80% Complete

Area B – Brick Progress



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Storm Work – Foundation for Site Wall



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

Duquesne Light Complete Work – Permanent Power



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

OVERALL PROGRESS



Upcoming Work:

- Complete Mechanical, Electrical and Plumbing Rough In at Area B
- Start Kitchen Equipment
- Area A – Fireproofing
- Area A - Roofing
- Start Mechanical, Electrical and Plumbing Rough In at Area A
- Complete Painting & Tile 2nd Floor Area C
- Complete Painting & Tile 3rd Floor Area C
- Complete Window installation at Area C
- Complete block and brick installation
- Concrete Slab on Grade in Gym
- Playground Surfacing

Project Schedule

- Mucci's schedule update dated 5/8/2026 shows Area A completing in September.
- HHS DR, District, Mucci & MCMS will review progress on 6/1/2026. Recommendations to be made to Board in June.



Project Stats:

- Project is at 144 day with no recordable injury



HHS DR
ARCHITECTS
ENGINEERS



Massaro
CM SERVICES, LLC

THANK YOU!

QUESTIONS?

